



# Agenda item 7a

**Austin WATER**  
Clearly Reliable

## WTP4 – Jollyville Transmission Main


Monthly Briefing  
Environmental Board  
June 20, 2012

**Water Treatment Plant 4** 

  
www.austintexas.gov/water



**Austin WATER**  
Clearly Reliable


### JTM Current Status (yellow) as of 6/13/12

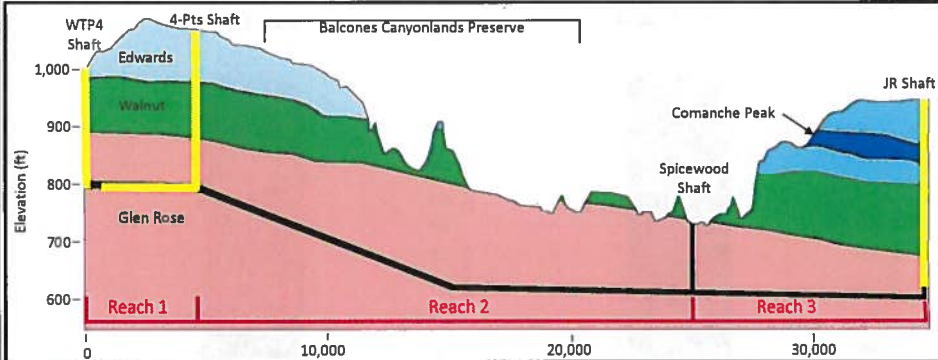

Reach 1 is 81% complete  
WTP4 Shaft is excavated, casing being installed this week  
JR Shaft is 96% complete

www.austintexas.gov/water

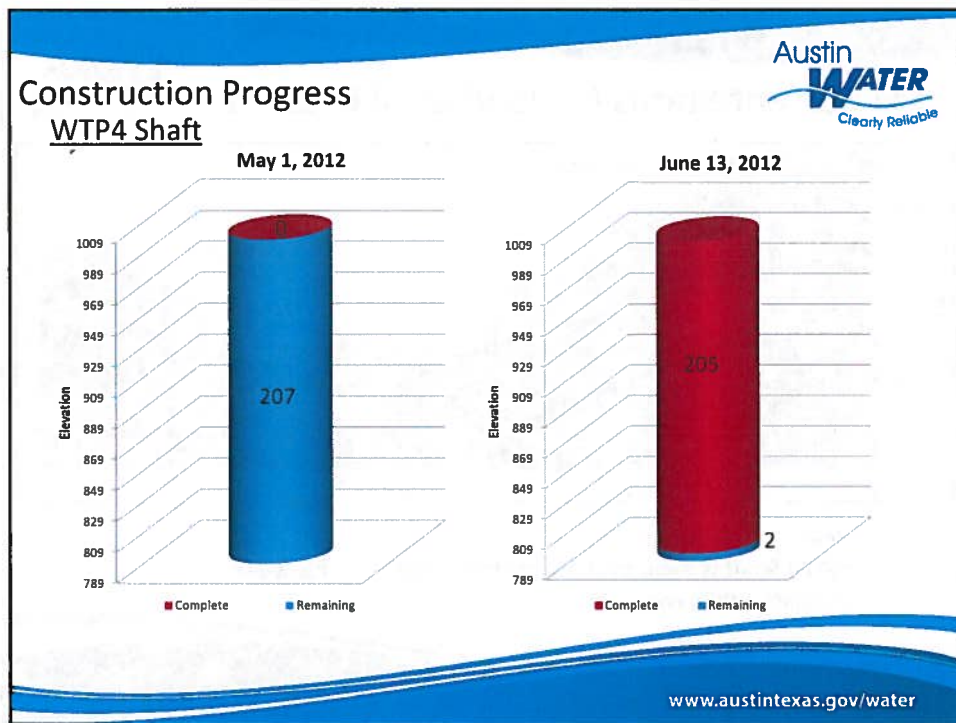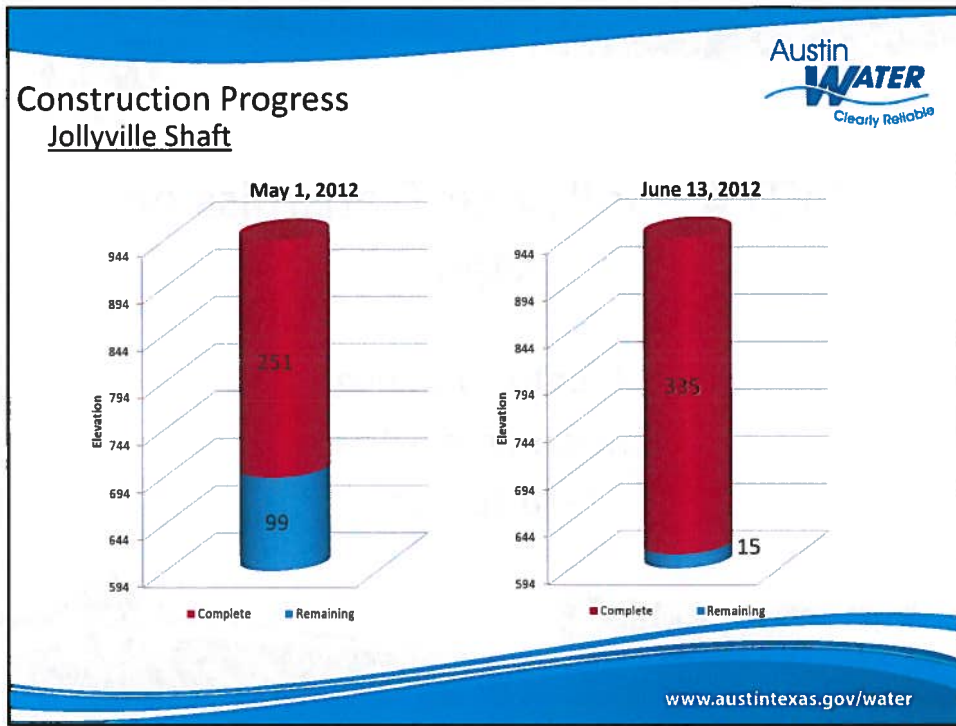

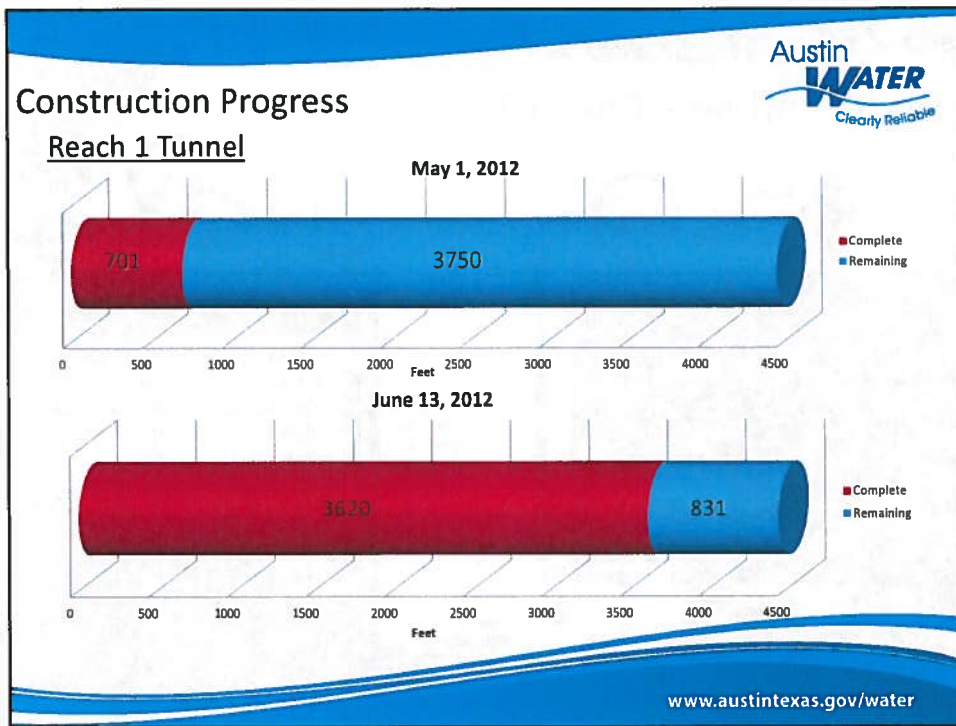


**Jollyville Transmission Main**

Projected Activities

- Jollyville Shaft Completion – Late June
- Reach 3 Starter/Tail Tunnel Excavation Start – Early July
- Spicewood Shaft Excavation Start – Mid July
- WTP4 Shaft Completion – Mid June
- Reach 1 Tunneling Completion – Late June
- Reach 2 Tunneling Start – Late July

www.austintexas.gov/water

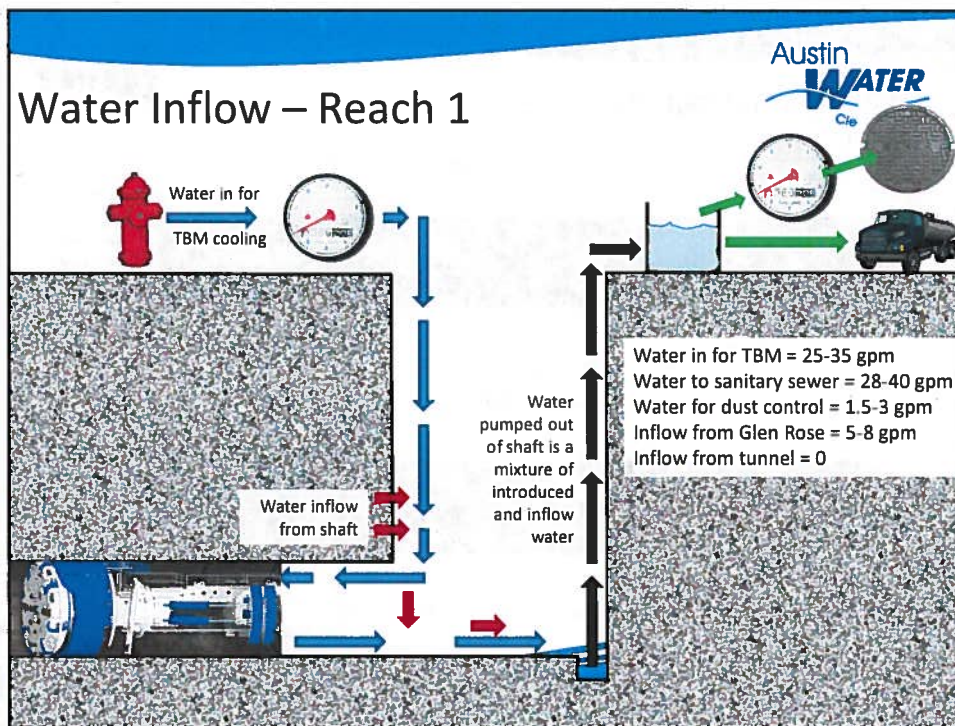

## Environmental

### Spoils Management

- Disposal at permitted locations
- ME Ruby pit & two development projects

### Downhole Camera at WTP site

- CCR 10(a) permit compliance and permeable ring
- No voids encountered for endangered species investigation

[www.austintexas.gov/water](http://www.austintexas.gov/water)



# Questions?

info@wtpfour.com

<http://austingo.austintexas.gov/department/water>



[www.austintexas.gov/water](http://www.austintexas.gov/water)

