


Airport Expansion and Development Program (AEDP) Active Projects Update

Airport Advisory Commission, April 2024

Lyn Estabrook – Deputy Chief Development Officer



**JOURNEY
WITHAUS**

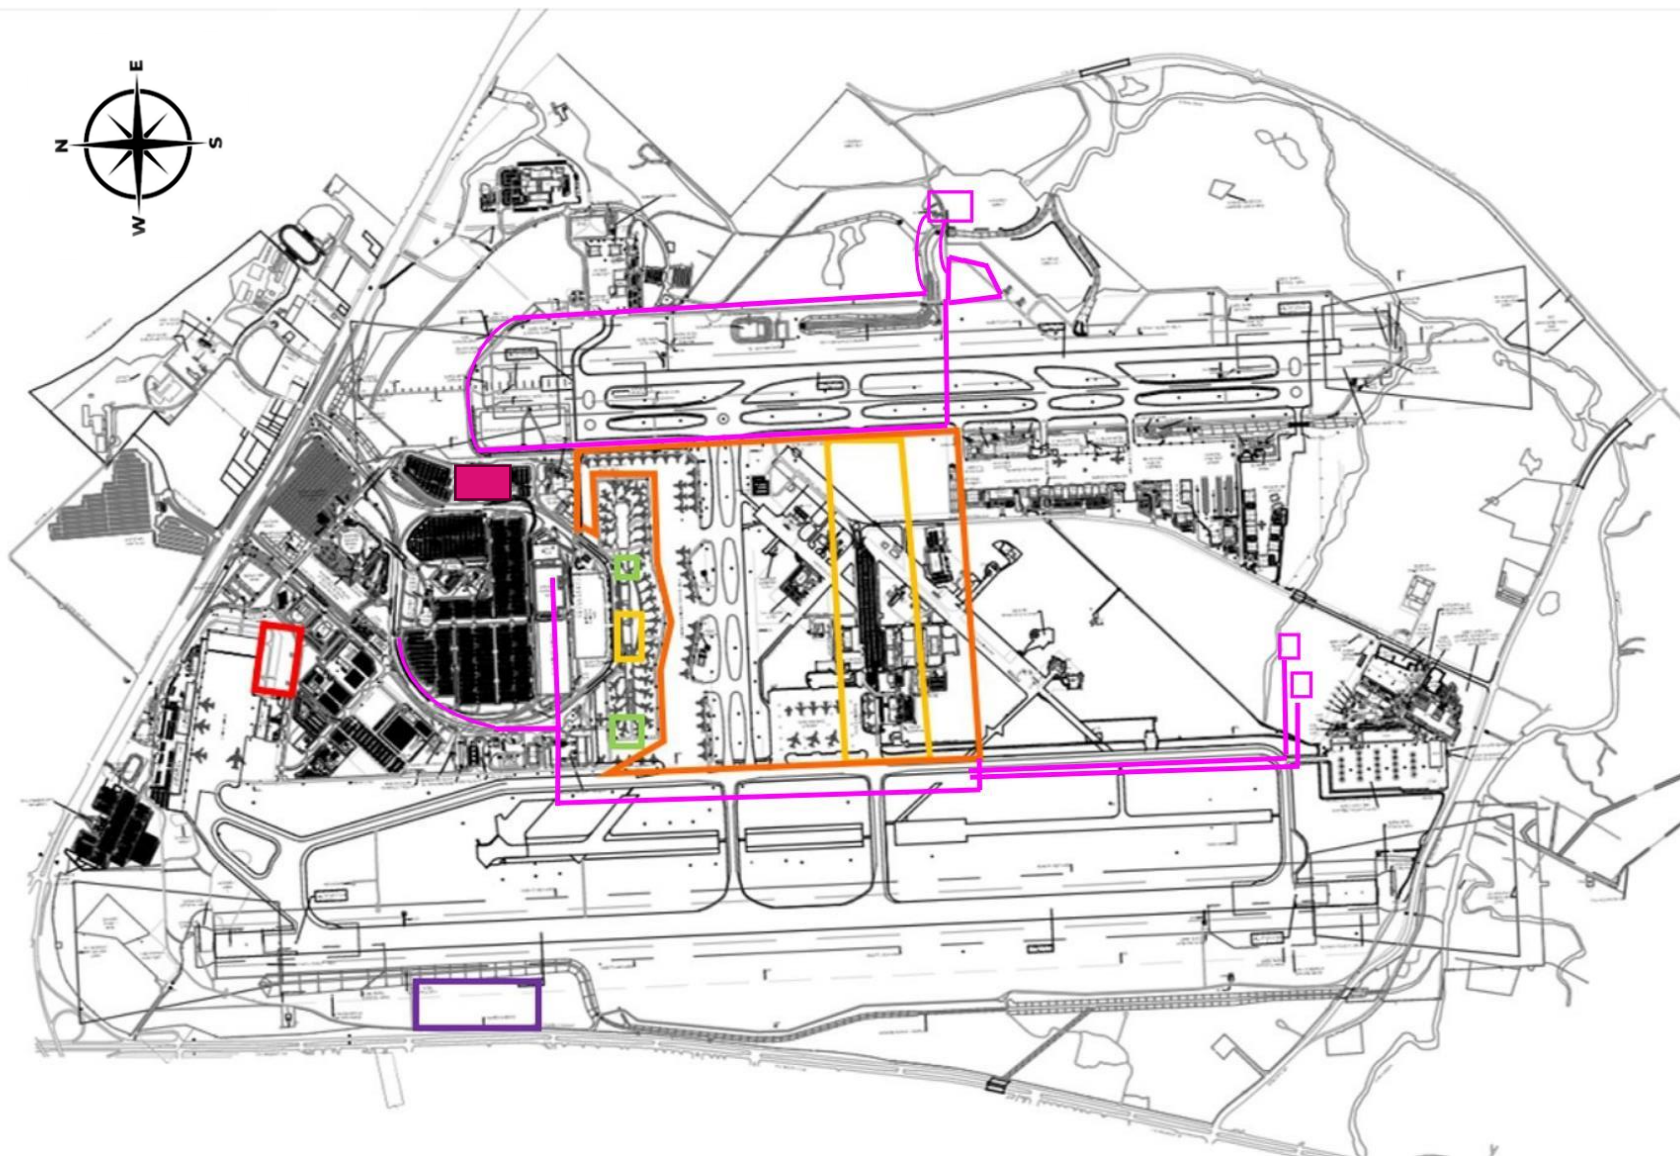

LEGEND

- **AEDP Airfield Infrastructure – Midfield Taxiways**
- **AEDP Building Demolition (locations shown on slide)**
- **Cargo Development East**
- **West Gates Expansion / Gate 13**
- **Midfield Investigations & Vehicle Checkpoints**
- **Existing Terminal Baggage Handling System Upgrades**
- **AUS Fuel Facility Phase 2 (Tenant led, AUS Fuels Project)**
- **Utility Infrastructure Campus-Wide UICW**
- **Relocate Central Utility Plant**

Midfield Investigations and Vehicle Checkpoints

Champion Sponsor – Towanda Cordon

Project Manager – Torrey Henson

Project number – 6000.121

Description: This project will expand guard-shacks at two vehicle Checkpoints, Alpha and Charlie, to allow efficient and secure access to the Aircraft Operations Area. The Midfield survey scope has been completed.

Risk	Mitigation
Checkpoints A & C Design underway. The Aircraft Operations Area must remain secure. All activities remain operational during construction phase.	Work with project teams and stakeholders, and tenants prior to construction beginning. Provide alternative routes to access the Aircraft Operations Area and increase security awareness to contractors during construction phase.

Status: The design for both Checkpoints Alpha and Charlie have been completed and approved by AUS. Consultant is currently making final revisions to Project Manual and will submit to CoA Quality Review Office for final review within the coming weeks. Checkpoints , funding, bidding, and construction has been placed on hold until project team receives approval from AUS executive team to move project into next phase.



%MWBE:
Design: 73%
Construction: TBD
%

Delivery Methods:
Design: GARVER
Construction: DBB

Project Budget:
Spend-To-Date: \$2,783,706
Obligated: \$3,188,436
Total Budget: \$6,300,000

Project Schedule:

[illegible]

AEDP Airfield Infrastructure – Utility Infrastructure Campus-Wide (UICW)

AUS Project Lead – Ellen Brunjes-Brandt
Project Manager – Marwa Ayad
Project number – 13307.001

Description – The Utility Infrastructure Campus-Wide (UICW) project involves the expansion or enhancement of existing and newly proposed utilities to meet the growing demands of the airport. The project encompasses utility systems including reclaimed water, storm drainage, water quality pond/deicing pond, detention pond, hydronic piping (chilled and hot water), AUS medium voltage electrical power distribution center, ductbank, and electrical distribution system, redundant electrical duct banks, information technology/telecommunications duct banks, and other utility extensions that may be identified as the AEDP program progress and their seamless coordination with other AEDP facilities projects.

Other Notes: This is an enabling project for AEDP Program specifically Concourse B, AD Hall, and Central Utility Plant Relocation Projects

Risk	Mitigation
Unforeseen Underground UTL	Include Survey in the design scope

Status:

- UICW Professional Engineering Services interviews **05April24**
- UICW Construction Manager at Risk Solicitation due 25March24
- UICW Received appropriation approval for fiscal year 2024 and 2025

%DBE:

Design: 5.75%

Construction: 6.32%

Delivery Methods:

Design: TBD


Construction: Construction Manager At Risk (CMR): TBD

Project Budget:


Spent To Date: \$0

Obligated: \$0

Total forecast Budget: \$164M

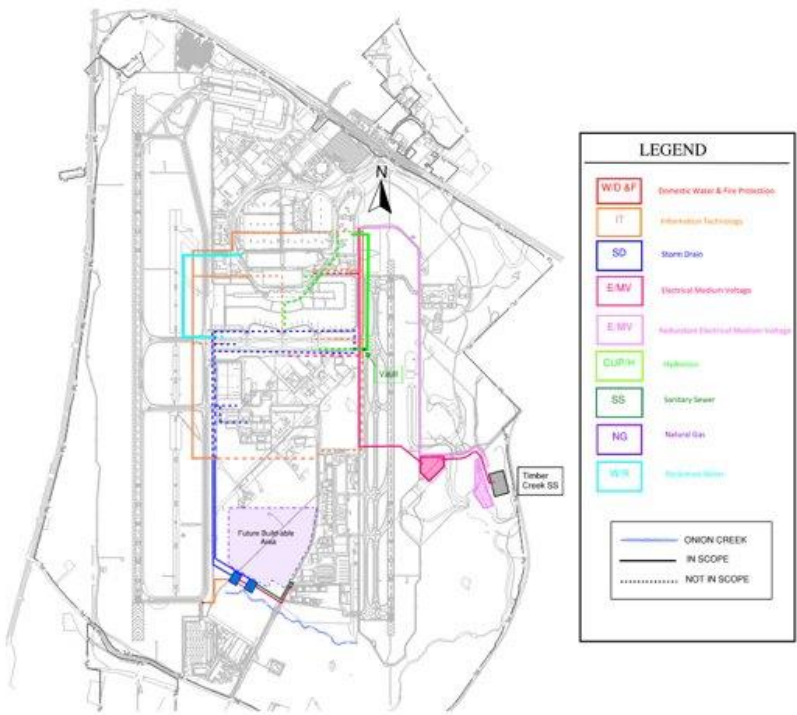

Project Schedule:

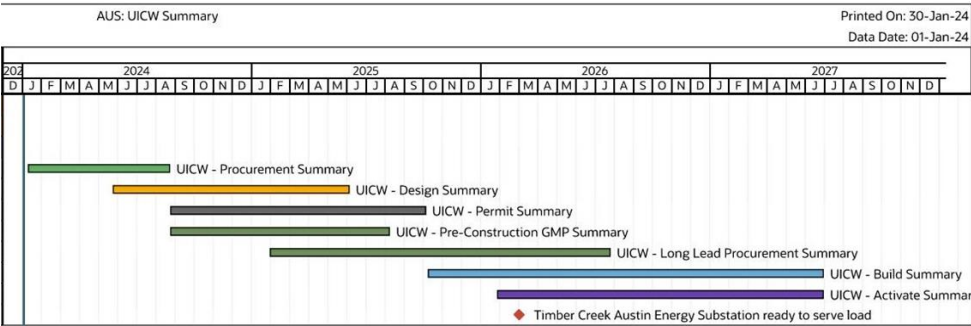


AEDP Airfield Infrastructure- Central Utility Plant (CUP)

AUS Project Lead – Ellen Brunjes-Brandt
Project Manager – Carol Stewart
Project number – 13307.002

Description: Description: Design, construct and commission a new, appropriately sized CUP and associated Thermal Energy Storage (TES) utilizing current efficiency technology, equipment, and operational processes to provide reliable, redundant and resilient service for the existing and future AUS cooling and heating loads.

Risk	Mitigation
Changing program will require update of load calculations	Monitor size of programmed buildings
Availability of Lot J for start of construction in June 2025	Landside Planning Task Force

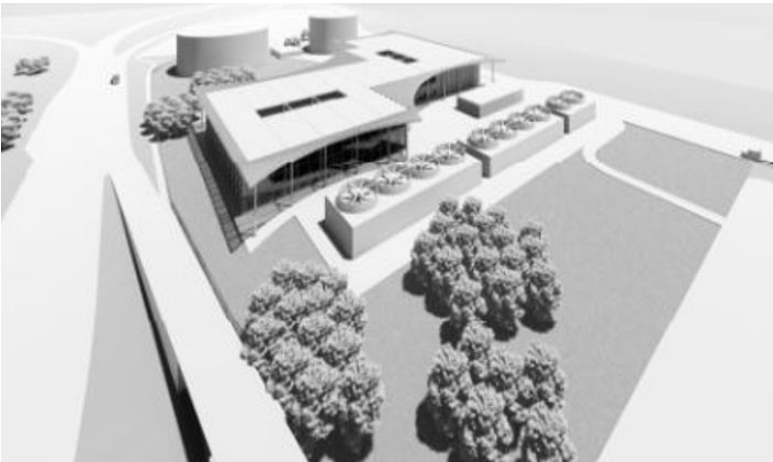

%DBE:
Design: 8.21%
Construction: TBD%


Delivery Methods:
Design: Design Build
Construction: Design Build

Project Budget:
Spent To Date: \$0
Obligated: \$485,000
Total Budget: \$200,232,000

Status:

- 01/12/24: received 6 Design Build proposals
- 01/17/24-02/28/24: Evaluation of proposals including interviews
- 03/15/24: RCA Due
- 03/22/24-05/02/24: Contract Development
- 04/10/24: Airport Advisory Commission Date
- 04/18/24: Council Date
- 05/16/24: Final Fee Proposal Due
- 06/06/24: Contract Execution

Project Schedule:

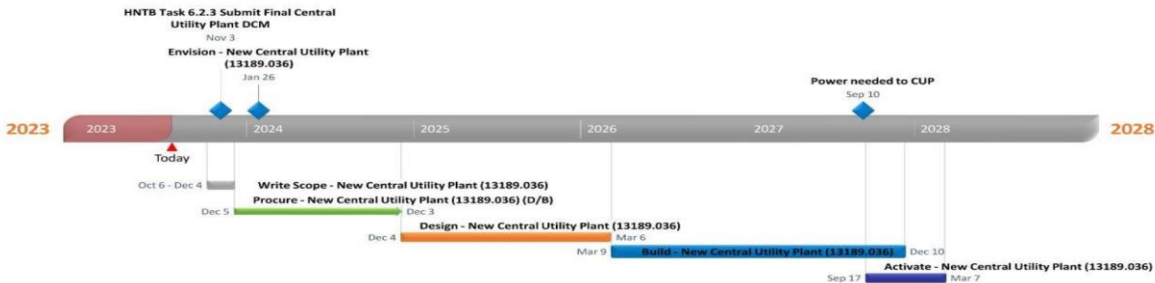

West Garage – Lot B

AUS Project Lead – Robert Mercado
Project Manager – Steven Latman
Project number – 13308.002


Description: Planning, design and construction of a multi-level parking garage with a capacity of approximately 7,700 spaces. The designated location for this garage is the current Lot B surface parking area (approx. 326,000 sf), situated directly north of the existing Blue Garage.

Other Notes: This project creates additional parking to replace parking and revenue lost due to construction and to meet future demand connected with enplanement growth forecasts associated with the addition of Concourse B

Risk	Mitigation
It is imperative to ensure close coordination between the design and construction of the garage with both ongoing and upcoming strategic projects	The project team will develop a strategic plan for a phased and staged approach to minimize disruptions to ongoing operations and activities at the Airport.

Status:

- Solicitation For Design Consultant received 4 proposals. Winning proposal has been selected.
- Solicitation For CMAR received 3 proposals. Winning proposal to be selected

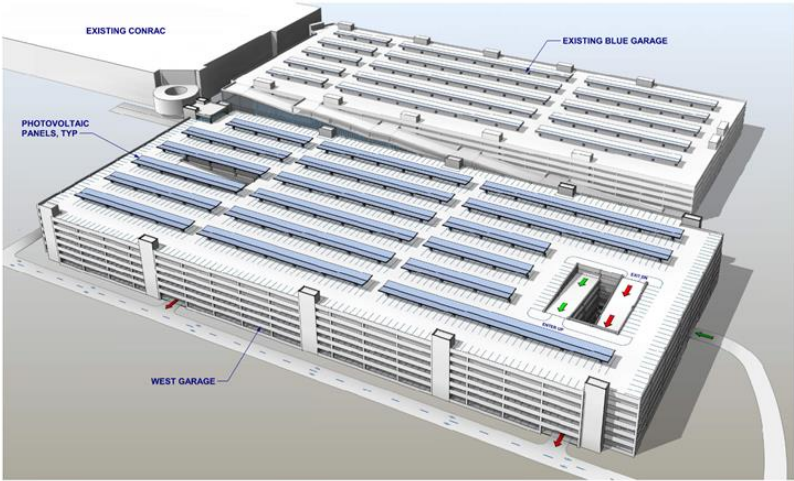


%MWBE:
Design: 10.54%
Construction: 14.27%

Delivery Methods:
Design: TBD
Construction: Construction;
Construction Manager At Risk
(CMAR): TBD

Project Budget:
Spent To Date: \$0
Obligated: \$19.7M
Total forecast Budget: \$288M

Project Schedule:



AEDP Building Demolition



Champion Sponsor – Lyn Estabrook
Project Manager – Ellen Brunjes-Brandt
Project number – 13189.012

Description: Demolish 39 Buildings on South Campus that are a safety hazard, original Airforce infrastructure, no longer serve operational need for the Department of Aviation and to make way for future development. The work includes removal of the facilities to slab level and disconnection of utilities throughout the site.

Risk	Mitigation
Power to lights in the staff parking lots delayed	New trenching from meter and panel to staff parking Lot

- Status:**
- Phase 3 Punchlist- ongoing
 - Substantial Completion - January 2024

Project Schedule:

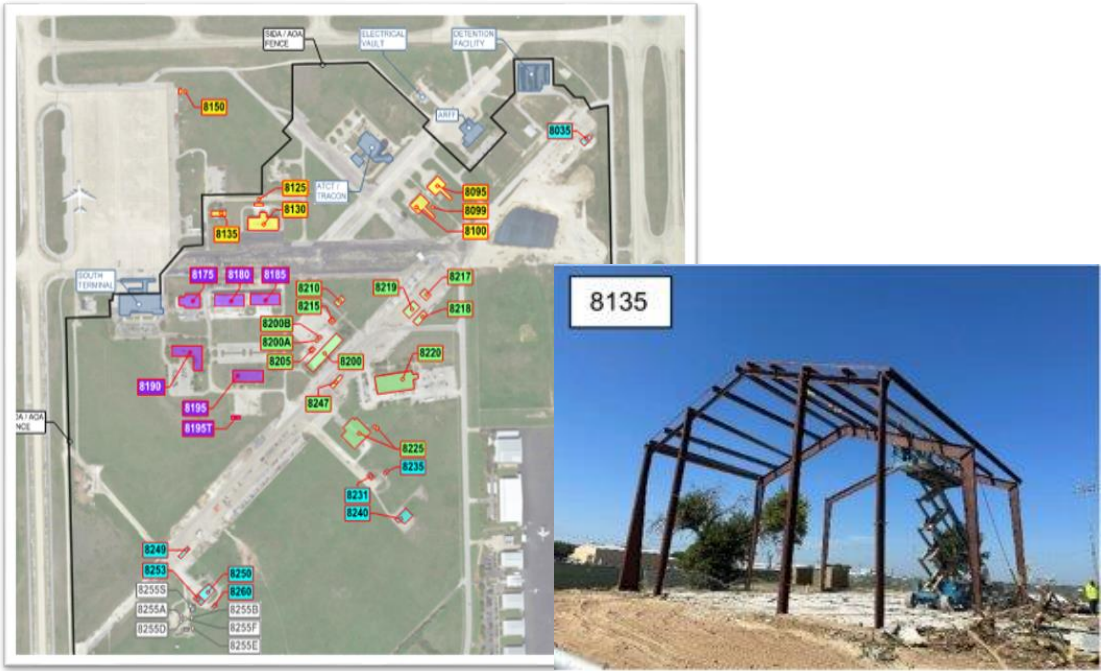

%MWBE:
Design: 15.8%
Construction: 26.87%

Delivery Methods:
Design: Corgan
Construction: Low Bid – STR Contractors

Project Budget:
Spend-To-Date: \$4,569,000
Obligated: \$5,312,000
Total Budget: \$9,608,000

Barbara Jordan Terminal Optimization West Gate Expansion

Champion Sponsor – Ghizlane Badawi
Project Manager – Robert Mercado
Project number – 13184.014


Description: The main expansion project will add 3 new Gates (short term) to the west end of the Barbara Jordan Terminal (BJT) and replace 12 aging boarding gates. This project will provide infrastructure needed for passenger growth, comfort, health and safety.

Risk	Mitigation
Coordination issues with Operations that affect construction timing and schedule.	Constant communication and notification among all stakeholders on aviation activities and project needs.

Status:

- Temporary Gate 34 and 36 are now open for use
- Apron Concrete and Trench Drain modifications underway.
- Pier Drilling for structure are ongoing.

Project Schedule:



%MWBE:
Design: 17%
Construction: 11.12%

Delivery Methods:
Design: Page Architects
(Rotation List A/E Prof Services)
Construction: Hensel Phelps
(CMR Selection)

Project Budget:
Spent-To-Date: \$26,475,344
Obligated: \$137,012,510
Total Project Cost : \$164,399,584

AUS Cargo Development East


Project Manager – Robert Mercado
Project number – 13189.026

Description: A 90,000 SF facility for operators/tenants with room to expand to 99,000 SF. Includes employee parking, truck staging, drainage infrastructure, 3 aircraft parking positions.

Risk	Mitigation

- Status:**
- Installation of MEP scopes and security systems underway.
 - Substantial Completion estimate – April 2024.

Project Schedule:



%MWBE:

Design: 15.8%

Construction: 1.13%

Anticipated Construction: 7.36%

Delivery Methods:

Design: Atkins

Construction: JE Dunn & Flintco

Project Budget:

Spend-To-Date: \$29,777,326

Obligated: \$31,738,412

Total Budget: \$32,874,000

AUS Fuel Facility Upgrade Package 2

Sponsor – Tenant Project - Airline Fuel Consortium
AUS Project Manager – David Smythe-Macaulay
Project number – F7003.08

Description: Project is led by tenant AUS Fuels LLC an Airline Fuel Consortium to design and build a new Jet A fuel storage facility with two underground transfer lines connecting to the existing facility.

Risk	Mitigation
Complete the "Decorative Fence Structure" soon after completion of the fuel storage facility.	Work with tenant and their Design-Builder to design and construct a decorative fence structure.

Status:

- Started filling tanks with fuel
- Completed renovations to the Metropolis & HWY 183 intersection
- Completed dike walls surrounding the tanks
- Completed all piping, pumps and buildings
- Continue with site grading, roads and rain gardens
- Project completion is anticipated at end of March 2024
- Monthly construction updates available online – SpeakUpAustin.org/AUSFuel

Project Schedule:

Task Name	2022			2023				2024			
	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Build	Build							Build			
Activate							Activate				



%MWBE
Goal: 6.6%
Participation to Date: 4.60%
Anticipated Participation: 5.10%

Delivery Methods: **Project Budget:**
Design-Build Contractor: ~\$64M
Burns & McDonnell

Existing Terminal Centralized Baggage Handling System Upgrades




Sponsor – Brian Long
AUS Project Manager – Rohini Kumarage
Project number – 5415.112

Description – Design build a new centralized baggage handling system (BHS) to increase screening capacity, address existing operational concerns, and upgrade to 30 Million Annual Passengers processed. Rebased line scope for Design of infill and bump out per AUS executive team and airlines in December 2022

Risk	Mitigation
Construction material shortage and lead/delivery times. Schedule extension due to redefined scope at the West Infill scope, may added 12 months. The EDS equipment delivery date is being coordinated with TSA	Ordering all equipment and materials early, tracking material pricing and procurement/delivery times. Ensured Phase 1 not impacted. West Infill release of 30% design to finalize the end product. Team is evaluating testing schedule to accommodate the delivery of the EDS machines.

Delivery Method: Design-Build	Project Budget:	%MWBE
Contractor: Whiting-Turner	Spend-To-Date: \$ 84,929,921	Construction and
Designers: Gensler, VTC BHS	Obligated: \$142,497,539	Design: 5.52%
	Total Budget: \$238,000,00	Anticipated: 10%

Project Schedule:

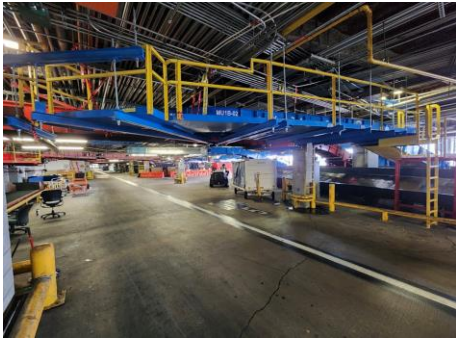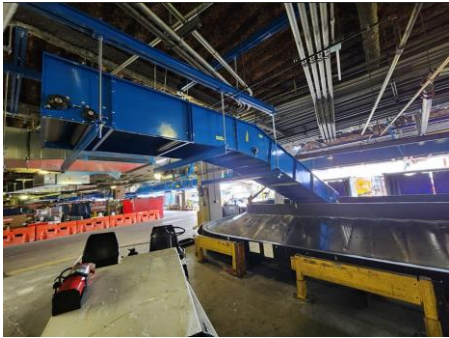

Status:
Tenant/Enabling - All Tenants have been relocated.
Phase 1 – 100% Baggage Handling System Design Approved by TSA, Conveyor Installation is 95% in Bag Claim Ceiling, 100% in the CBIS/CBRA, and 75% in the Apron. Electrical Installation is 98% CBIS/CBRA with device terminations. Conveyor start Up and programing in progress.
Phase 2 –West Infill/Bump out Concept Planning redefined per AUS Exec and Airlines due to increased passenger demand. Additional funding was approved from AAC and Council. BHS CBIS /CBRA was approved by TSA. 60% design was submitted and reviewed by AUS. Permits submissions for early works site-work and demolition have been submitted and approved. Contractor for sitework has mobilized and has cleared the site. Underground utilities have commenced.
Budget: Phase 1 on track, Phase 2 pending 100% drawings (redesign of bump out).

Thank You!

**JOURNEY
WITHAUS**
