1 - Preliminary

Project Name: ABIA Parking Garage and Rental Car Facility Project Sponsor/Client: Aviation Parking

(CONRAC)

Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$2,000,000

ABIA Number: L3162 DOA PM: Janice White PWD PM: Robert Pirtle

FDU Number: 4910-8107-3162 Sub-project ID: 6001.006 Grant Number: NA

Project Status: Project team meetings were held in March.
Ongoing meetings are being held in order to reach agreement on business terms.

Reimbursement agreement is currently under review for approval.

Parking study and traffic study documents are to be submitted by PGAL.

Project Name: Baggage System Servers Project Sponsor/Client: Aviation IS

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$400,000

ABIA Number: T3192 DOA PM: Robert Hengst PWD PM:

FDU Number: 4910-8107-3192 Sub-project ID: 5415.061 Grant Number: NA

Project Status: Test platform hardware from NEC arrived. Siemens is working on a proposal to do the research and

development for migrating our software platform to the new hardware.

Project Name: Information Technology Master Plan Project Sponsor/Client: Aviation IS

Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$1,000,000

ABIA Number: L3188 DOA PM: Jonathan Lian PWD PM:

FDU Number: 4910-8107-3188 Sub-project ID: 6001.072 Grant Number: NA

Project Status: Discussions with stakeholders have begun. In April we will ask Public Works to assign a PM and CLMD

to start the RFQ process.

Project Name: Neutral Host System Project Sponsor/Client: Aviation IS

Project Type: 6501 - Other Improvements Total Project Estimate: \$700,000

ABIA Number: T3107 DOA PM: Robert Hengst PWD PM: NA
FDU Number: 4910-8107-3107 Sub-project ID: 6501.011 Grant Number: NA

Project Status: Purchasing of equipment is ongoing by IS.

2 - Design/Study

FDU Number:

ABIA Number:

Project Name: ABIA Campus Signage Improvements Phase 2 Project Sponsor/Client: Aviation

Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$3,000,000

ABIA Number: L3180 DOA PM: Janice White PWD PM: Robin Camp

FDU Number: 4910-8107-3180 Sub-project ID: 6001.068 Grant Number: NA

Project Status: Directory and directional signage presented to executive team for input.

Landside signage presented for the first time to project team for input/update. Project team preparing additional information for next steps on each effort.

Project Name: ABIA Terminal Fire Protection Improvements - Ph. Project Sponsor/Client: Aviation

4910-8107-3176

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$5,700,000

T3176 ABIA Number: DOA PM: Ben Avila PWD PM: Robert Pirtle

Sub-project ID:

Project Status: Project PRELIM Phase work is in progress for study of ABIA Terminal Bldg dry fire sprinkler systems.

PER work expected to be completed in APR-2011 and 95% PER submitted in MAY-2011.

5415.056

Grant Number:

PWD PM:

Project Name: ABIA Wildlife Hazard Assessment Project Sponsor/Client: Aviation

Project Type: 5702 - Stormwater/Environmental Improvements Total Project Estimate: \$266,667

ABIA Number: M3179 DOA PM: Joe Medici PWD PM: Jules Parrish

Grant Number: 4910-8107-3179 FDU Number: Sub-project ID: 6000.054 55

Wildlife survey was done in March. Next site survey to be conducted 12th and 14th of April. FAA has Project Status:

approved the aGIS SOW submittal. (01APR2011).

Airfield Lighting Control and Monitoring System Project Sponsor/Client: Aviation **Project Name:**

Total Project Estimate: \$1,100,000 Project Type: 6000 - Airside Improvements

PWD PM: Robin Camp ABIA Number: A3142 DOA PM: Robert Hengst

FDU Number: 4910-8107-3142 Sub-project ID: 6000.047 Grant Number:

Project Status: 90% documents are currently under review.

Project Name: Baggage Management Office Indoor Air Quality Project Sponsor/Client: Aviation

Improvements

L3143

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$150,000

T3184 DOA PM: Ben Avila PWD PM: TBD ABIA Number:

FDU Number: 4910-8107-3184 Sub-project ID: 5415.058 Grant Number:

Project Status: IFB docs submitted by Sunland in MAR-2011 and provided to CLM CoA JOC Mgr on 3-30-2011 for

RFP. JOC assignment process in progress. Consultant obtaining CONST work permit.

Project Name: Cooling Tower Repairs Project Sponsor/Client: Aviation

Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$200,000

DOA PM: Ben Avila FDU Number: 4910-8107-3143 Sub-project ID: 6001.063 Grant Number: NA

Project Status: Preliminary Engineering Report Completed and waiting for bid/award/execution of the recommended

work, perhaps by using CoA Job Order Contract.

Project Name: Drainage Master Plan Project Sponsor/Client: Aviation Project Type: 5702 - Stormwater/Environmental Improvements Total Project Estimate: \$765,000 ABIA Number: M3139 DOA PM: Joe Medici PWD PM: Robert Pirtle FDU Number: 4910-8107-3139 Sub-project ID: 5702.007 Grant Number: NA Project Status: Final draft report due Monday, April 4. Legal has provided Asviation staff first draft of ordinance language - staff to provide review comments by 4/8. (040111) **Project Name: Environmental Management System** Project Sponsor/Client: Aviation \$600,000 Project Type: 5702 - Stormwater/Environmental Improvements Total Project Estimate: ABIA Number: M3151 DOA PM: Kane Carpenter PWD PM: NA FDU Number: 4910-8107-3151 Sub-project ID: 5702.008 Grant Number: NA Project Status: NTP issued for PRELIM Phase services to RS&H in 1-12-2011. Work ongoing.

General Aviation Apron Rehabilitation Project Sponsor/Client: Aviation **Project Name:** \$1,000,000 Project Type: 6000 - Airside Improvements Total Project Estimate: ABIA Number: A3147 DOA PM: Robert Hengst PWD PM: Craig Russell FDU Number: 4910-8107-3147 Sub-project ID: 6000.050 Grant Number: NA

Project Status: ESD is finalizing the design with expected construction to start Fall 2011.

Project Name: IS Bldg 7355 Fire Protection Improvements Project Sponsor/Client: Aviation IS Project Type: 6501 - Other Improvements Total Project Estimate: \$500,000 ABIA Number: P3141 DOA PM: Stephen Dick PWD PM: Burton Jones FDU Number: 4910-8107-3141 Sub-project ID: 6001.062 Grant Number:

UPDATED on 4-3-2011 by B Avila - After months of delays, DESIGN Phase NTP to be issued to Project Status: Sunland Group by CLM on 03-16-2011. DESIGN Phase Kick-off mtg held on 03-17-2011. Work in

progress.

Project Name: IS Building 7355 Emergency Power Improvements Project Sponsor/Client: Aviation IS Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$750,000 ABIA Number: L3163 DOA PM: Ben Avila PWD PM: Burton Jones

FDU Number: 4910-8107-3163 Sub-project ID: 6001.067 Grant Number: NA

Project Status: Elect Study - Initial 65% PER submitted in MAR-2011 and rejected as incomplete by DoA. Resubmittal issued on 3-31-2011 for Owner review. Forwarded \$4K fee to Austin Energy for duel power

feed study to IS Bldg 7355. Study in progres and due in MAY-2011. 2. Office Add - Consultant proposal submitted and approved by DoA in MAR-2011. NTP issued to by

CLM to Sunland on 2-25-2011. Work is in progress.

3. Bldg Expand - Sunland proposal for this study expected in APR-2011.

Project Name: Landside Job Order Contracting (JOC) Projects Project Sponsor/Client: Aviation Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$250,000

ABIA Number: L3189 PWD PM: NA DOA PM: Various

FDU Number: 4910-8107-3189 Sub-project ID: Grant Number: NA 6001.073

JOC-1: A/E presented initial design considerations for phase 1. Project Status:

Follow-up meetings are being scheduled.

Project Name: Master Plan Level 1 Project Sponsor/Client: Aviation
Project Type: 5415 - Terminal Improvements Total Project Estimate: \$1,393,000

ABIA Number: T3103 DOA PM: Joe Medici PWD PM:

FDU Number: 4910-8107-3103 Sub-project ID: 5415.025 Grant Number: NA

Project Status: Final payment to CADD Studios pending. Requested updated from Public Works PM. (01APR11)

Project Name: Overflow Parking Lot Project Sponsor/Client: Aviation Parking

Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$9,000,000

ABIA Number: L3133 DOA PM: Dale Thompson PWD PM: Pirtle (Ph 1); Wepryk (Ph 2)

FDU Number: 4910-8107-3133 Sub-project ID: 6001.015 Grant Number: NA

Project Status: 1. ESD is preparing the plans for the parking on the Cargo Apron. PW PM has received approval to

use a cooperative procurement process for construction from CLMD.

It was requested that the rotation list authority be increased for RS&H to do Phase 2.

It was requested that Phase 2 be a separate FDU.

Project Name: Terminal Area Spall Improvements Project Sponsor/Client: Aviation
Project Type: 5415 - Terminal Improvements Total Project Estimate: \$165,000

ABIA Number: T3172 DOA PM: Ben Avila PWD PM:

FDU Number: 4910-8107-3172 Sub-project ID: 5415.054 Grant Number: NA

Project Status: PRELIMINARY Phase work being provided under 3149 project (See 3149 project for info).

Project Name: Terminal Curbside Guard Rail Improvements Project Sponsor/Client: Aviation
Project Type: 5415 - Terminal Improvements Total Project Estimate: \$120,000

ABIA Number: T3169 DOA PM: Ben Avila PWD PM:

FDU Number: 4910-8107-3169 Sub-project ID: 5415.051 Grant Number: NA

Project Status: PRELIMINARY Phase work being provided under 3149 project (See 3149 project for info).

Project Name: Terminal Electrical System Reliability Project Sponsor/Client: Aviation

Improvements

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$170,000

ABIA Number: T3168 DOA PM: Ben Avila PWD PM:

FDU Number: 4910-8107-3168 Sub-project ID: 5415.050 Grant Number: NA

Project Status: PRELIMINARY Phase work being provided under 3101 project (see 3101 project for Elect Study info).

Project Name: Terminal Emergency Power Improvements Project Sponsor/Client: Aviation
Project Type: 5415 - Terminal Improvements Total Project Estimate: \$170,000

ABIA Number: T3170 DOA PM: Ben Avila PWD PM:

FDU Number: 4910-8107-3170 Sub-project ID: 5415.052 Grant Number: NA

Project Status: PRELIMINARY Phase work being provided under 3101 project (see 3101 project for Elect Study info).

Project Name: Terminal Expansion Joint Improvements Project Sponsor/Client: Aviation

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$675,000

ABIA Number: T3167 DOA PM: Ben Avila PWD PM:

FDU Number: 4910-8107-3167 Sub-project ID: 5415.049 Grant Number: NA

Project Status: PRELIMINARY Phase work being provided under 3149 project (See 3149 project for info).

AVIATION PROJECTS STATUS REPORT

Terminal HVAC Unit Access Improvements Project Name:

Project Sponsor/Client: Aviation

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$1,500,000

ABIA Number:

T3171

DOA PM: Ben Avila

PWD PM: Burton Jones

FDU Number:

4910-8107-3171

Sub-project ID: 5415.053 Grant Number:

Project Status: DESIGN kick-off mtg held in FEB-2011. Work in progress.

PRELIM design docs due in APR-2011.

Project Name: Terminal IAQ Study 2010 Project Sponsor/Client: Aviation

Project Type:

6501 - Other Improvements

Total Project Estimate:

\$10,014

ABIA Number:

M2010.02

DOA PM: Kane Carpenter

PWD PM: NA

NA

FDU Number:

5070-8100-6400 Sub-project ID: Grant Number:

NA

Project Status:

Report was received and is being analyzed. The consultant will meet with groups to explain results and

any possible actions.

Project Name:

Terminal Improvements - 2009

Project Sponsor/Client: Aviation

Total Project Estimate:

\$500,000

Project Type: ABIA Number: 5415 - Terminal Improvements

DOA PM: Ben Avila

PWD PM: Robert Pirtle

FDU Number:

4910-8107-3149

Sub-project ID: 5415.024

Grant Number: NA

Project Status:

Item 1 - Term Exp Jt: DoA staff to review existing it installation in APR-2011 and provide comments to

consultant.

T3149

Items 2-3-4 - Guard Rail Imp - Bldg Spalling - Road Exp Jt: Consultnat to submit proposal to prep

CONST docs for this work in APR-2011.

Item 5 - BMO IAQ Imp: See 3184 for work status info.

Item 6 - Roadway Spalling: FINAL PER submitted on 3-29-2011 and approved by DoA. Proposal for CONST Phase work due in APR-2011. DoA Maint providing some temporary netting in APR-2011 to

reduce risk of falling debris from elevated roadway.

7. Garage Bridge Spalling - DoA approved Sunland proposal for PRELIM Phase services in MAR-

2011. NTP issued by CLM for PRELIM Phase services on 3-31-2011. Work in progress.

Project Name:

5415 - Terminal Improvements

Terminal Roadway Expansion Joint Rehabilitation Project Sponsor/Client: Aviation Total Project Estimate:

\$300,000

Project Type: ABIA Number:

DOA PM: Ben Avila

PWD PM:

FDU Number:

T3173

4910-8107-3173

Sub-project ID: 5415.055

Grant Number: NA

Project Status:

PRELIMINARY Phase work being provided under 3149 project (See 3149 project for info).

3 - Bid/Award/Execution

Project Name: ABIA Terminal Improvements 2006 - Ph 4

Project Sponsor/Client: Aviation

Project Type: 5415 - Terminal Improvements

Total Project Estimate: \$2,385,630

ABIA Number: T3

T3101 DOA PM: Ben Avila

PWD PM: Burton Jones

FDU Number:

4910-8107-3101

Sub-project ID: 5415.021

Grant Number: NA

Project Status:

1. CONST Kick-Off Mtg to be set-up by PW PM in APR-2011.

2. FINAL PER for Elect Study approved by DoA. Will forward recommendation for implementing

improvements to DoA mgmt soon.

Project Name: GTSA Relocation and Renovation

Project Sponsor/Client: City of Austin / Aviat

Project Type:

6001 - Landside Facility Improvements

Total Project Estimate: \$6,478,000

ABIA Number:

L3165

DOA PM: Richard Chaney

PWD PM: Robin Camp

FDU Number:

4910-8107-3165

Sub-project ID: 6001.069

Grant Number: NA

Project Status: Partnering Meeting was held on 25-Mar-2011. Pre-Construction meeting is being held on the 30th of March. Site Plan Correction approved on 29-Mar-2011, building permit pending. Contract has not been

excecuted.

Project Name: Remain Over Night Apron, Phase 2

4910-8107-3156

Project Sponsor/Client: Aviation

Project Type:

6000 - Airside Improvements

Total Project Estimate:

\$9,500,000

\$750,000

NA

ABIA Number:

A3156

DOA PM: Dale Thompson

PWD PM: Robert Pirtle

FDU Number:

Sub-project ID: 6000.051

Grant Number: 55-10

Project Status: This phase of the project includes the civil design and pavement construction for aircraft parking. Bids

were opened on March 17, and the low bidder is Austin Bridge & Road. Next tasks are airport

commission and City Council action, for contract award and execution.

Project Name: T

Terminal Job Order Contracting (JOC) Projects

Project Sponsor/Client: Aviation

Project Type:

7719 - Terminal, Future

Total Project Estimate:

PWD PM: NA

ABIA Number: FDU Number:

4910-8107-3191

T3191

Sub-project ID: 5415.060

Grant Number:

Project Status:

Funding of \$250,000 moved from 4910-8107-3185.

JOC-1: Preconstruction meeting schedule for Prism. Approvals received so that work can begin.

Task Assignment X - Gas Piping Improvements (By B Avila):

DOA PM: Various

NTP for \$54,004 amount issued to Alpha by CLM under their CoA JOC contract on 3-21-2011. Sub-Comp date is 6-21-2011. CONST kick-off mtg held on 3-30-2011. Work planning in progress

4 - Construction

Project Name: ABIA Parking Lot Maintenance - 2010 Project Sponsor/Client: Aviation Parking

Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$1,476,006

ABIA Number: L3161 DOA PM: Robert Hengst PWD PM: Greg Johnston

FDU Number: 4910-8107-3161 Sub-project ID: 6001.052 Grant Number: NA

Project Status: Construction continues on schedule.

Project Name: ABIA Terminal Checkpoint Improvements Project Sponsor/Client: TSA

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$1,100,000

ABIA Number: T3181 DOA PM: Robert Hengst PWD PM: Alison Von Stein

FDU Number: 4910-8107-3181 Sub-project ID: 5415.057 Grant Number: NA

Project Status: The functional portions of the project were completed on time. Aesthetic completion will be by the first

week of April.

Project Name: Airside Demolition Project Sponsor/Client: Aviation

Project Type: 6501 - Other Improvements Total Project Estimate: \$775,000

ABIA Number: P3125 DOA PM: Dale Thompson PWD PM: Darryl Haba
FDU Number: 4910-8107-3125 Sub-project ID: 6000.045 Grant Number: NA

Project Status: Sisk-Robb was awarded a contract to demo Bldgs 2020, 8120 and 8145, along with structures

associated with the Noise Mitigation Project. Currently working on the demo of the former O Club / Golf

Clubhouse. Need to cap water lines in that area before the building can be removed.

Electrical service to Gate W250 comes from Bldg 8120, so staff is looking at options to re-route the

service line feed to the gate.

Project Name: Garage Repairs Project Sponsor/Client: Aviation

Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$3,724,436

ABIA Number: L3129 DOA PM: Dale Thompson PWD PM: Robin Camp
FDU Number: 4910-8107-3129 Sub-project ID: 6001.056 Grant Number: NA

Project Status: NTP issued 4/5/10. Coordination with RAC and parking operations is going well. Approximately 65% of

work complete. Anticipate project completion in June.

Project Name: Reclaimed Water Service Project Sponsor/Client: AWU / Aviation

Project Type: 6001 - Landside Facility Improvements Total Project Estimate: \$157,000

ABIA Number: L3108 DOA PM: Dale Thompson PWD PM: John Wepryk

FDU Number: 4910-8107-3108 Sub-project ID: 6001.053 Grant Number: NA

Project Status: Contractor is Cash Construction Company. Notice to Proceed for construction issued 2/1/2011.

Contractor continues work at Hornsby Bend, and with bore under the river. Expect irrigation

subcontractor to begin work on ABIA property on 4/7/11.

5 - Planning				
Project Name:	GTSA Relocation a	nd Renovation AIPP	Project Sponsor/Client:	AIPP
Project Type:	6001 - Landside Fac	cility Improvements	Total Project Estimate:	\$84,000
ABIA Number:	L3193	DOA PM: Matt Coldwell	PWD PM:	
FDU Number:	4910-8107-3193	Sub-project ID: 6001.069	Grant Number:	NA
Project Status:	AIPP work is being	managed by Matt Coldwell. Fund	s will be used when appropr	iate.
Project Name:	Terminal Improven	nents 2006 AIPP	Project Sponsor/Client:	AIPP
Project Type:	5415 - Terminal Imp	rovements	Total Project Estimate:	\$23,664
ABIA Number:	T3178	DOA PM: Matt Coldwell	PWD PM:	
FDU Number:	4910-8107-3178	Sub-project ID: 5415.021	Grant Number:	NA
Project Status:	AIPP work is being i	managed by Matt Coldwell. Fund	s will be used when appropri	iate.

6	_	On	ho	М
U	~	VII	110	14

Project Name: Central Utility Plant Piping Improvements

6001 - Landside Facility Improvements

Total Project Estimate:

\$170,000

ABIA Number:

L3164

DOA PM: Robert Hengst

Sub-project ID:

PWD PM:

FDU Number:

Project Type:

4910-8107-3164

6001.065

Grant Number: NA

Project Sponsor/Client: Aviation

Project Status:

Project Name:

Waiting to be assigned.

Project Sponsor/Client: Aviation

\$750,000

Project Type: ABIA Number:

5702 - Stormwater/Environmental Improvements

PWD PM:

FDU Number:

M3118

DOA PM: Robert Hengst

Total Project Estimate:

4910-8107-3118

Sub-project ID: 5702.006

Grant Number:

NA

Project Status: Work will commence when new Environmental staff is ready for project.

Grading & Drainage Improvements

Project Name: Landside and Parking Lot Improvements Project Sponsor/Client: Aviation Parking

Project Type: ABIA Number: 6001 - Landside Facility Improvements

Total Project Estimate:

\$1,290,000

L3186

DOA PM: Dale Thompson

FDU Number:

4910-8107-3186

Sub-project ID: 6001.070 Grant Number:

PWD PM: Robert Pirtle NA

Project Status:

Kickoff meeting was held with Parking. We are working on the scope of work and determining which

consultant method to use.

Follow-up meeting held on 2/11 with Parking and ESD. It was decided that the Cargo Apron Parking Project is a higher priority than this project, and efforts would be directed appropriately. Scope of work was further defined, however much remains to be determined, relative to the impact on this project by the CONRAC project.

Project Name:

Terminal Improvements and Repairs - FY 2011

Project Sponsor/Client: Aviation

Project Type:

5415 - Terminal Improvements

Total Project Estimate:

\$6,300,000

ABIA Number:

T3190

DOA PM: TBD

PWD PM:

FDU Number: Project Status:

4910-8107-3190 Sub-project ID:

5415.059

Grant Number: NA

7 - Post-construction

Project Name: ABIA Security System Upgrade Project Sponsor/Client: Aviation

Project Type: 6501 - Other Improvements Total Project Estimate: \$10,150,000

ABIA Number: U3106 DOA PM: Jonathan Lian PWD PM: Alison Von Stein FDU Number: 4910-8107-3106 Sub-project ID: 6501.017 Grant Number: 36, 38

Project Status: Warranty period ends 5/2011.

Project Name: ABIA Terminal Office-HVAC Improvements Project Sponsor/Client: Aviation

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$738,149

ABIA Number: T3135 DOA PM: Ben Avila PWD PM: David Taylor

FDU Number: 4910-8107-3135 Sub-project ID: 5415.044 Grant Number: NA

Project Status: Subproject has been closed. FDU close-out in progress.

Project Name: Airfield Lighting Improvements and Pavement Project Sponsor/Client: Aviation

Rehabilitation

Project Type: 6000 - Airside Improvements Total Project Estimate: \$7,429,238

ABIA Number: A3091 DOA PM: Dale Thompson PWD PM: Tony Krauss

FDU Number: 4910-8107-3091 Sub-project ID: 6000.028 Grant Number: 36, 41, 42, 43

Project Status: Subproject and FDU close-out in progress.

Project Name: Airfield PCC Joint Sealant Rehabilitation Project Sponsor/Client: Aviation

Project Type: 6000 - Airside Improvements Total Project Estimate: \$3,100,000

ABIA Number: A3146 DOA PM: Dale Thompson PWD PM: Robert Pirtle

FDU Number: 4910-8107-3146 Sub-project ID: 6000.049 Grant Number: 54

The Number. 4910-0107-0140 Gub-project Ib. 0000.049 Grant Number. 04

Project Status: Work is complete, and project closeout is in progress. Record drawings received on 2/22/11.

Project Name: Baggage Handling System Controls Project Sponsor/Client: Aviation

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$37,250

ABIA Number: T3148 DOA PM: Stephen Dick PWD PM:

FDU Number: 4910-8107-3148 Sub-project ID: 5415.046 Grant Number: NA

Project Status: Subproject has been closed. FDU close-out in progress.

Project Name: Baggage Screening Improvements Project Sponsor/Client: Aviation

Project Type: 5415 - Terminal Improvements Total Project Estimate: \$23,751,499

ABIA Number: T3072 DOA PM: Ben Avila PWD PM:

FDU Number: 4910-8107-3072 Sub-project ID: 5415.026 Grant Number: NA

Project Status: Subproject has been closed. FDU close-out in progress.

Project Name: Business Development / Properties Study Project Sponsor/Client: Aviation

Project Type: 6501 - Other Improvements Total Project Estimate: \$43,000

ABIA Number: M3182 DOA PM: Joe Medici PWD PM:

FDU Number: 4910-8107-3182 Sub-project ID: 6501.026 Grant Number: NA

Project Status: Final report has been submitted by the consultant 10/22/2010. Copies have been distributed and

reviewed by Executive staff. Final pay app has been processed. Project has been completed and is

closed. Reports and documentation provided to Document Control for filing. (30Nov10)

AVIATION PROJECTS STATUS REPORT

ject Name:	ERS Perimeter Roa	d Study	Project Sponsor/Client:	Aviation
ject Type:	6000 - Airside Impro	vements	Total Project Estimate:	\$3,169,962
A Number:	A3081	DOA PM: Dale Thompson	PWD PM: Tony	Krauss
J Number:	4910-8107-3081	Sub-project ID: 6000.027	Grant Number:	NA
ject Status:	Subproject has been	closed. Remaining balances ne	ed to be transferred.	
ject Name:	General Aviation Av	venue Pavement Rehabilitation	Project Sponsor/Client:	Aviation
ject Type:	6001 - Landside Fac	ility Improvements	Total Project Estimate:	\$501,139
A Number:	L3100	DOA PM: Dale Thompson	PWD PM: David	Taylor
J Number:	4910-8107-3100	Sub-project ID: 6001.033	Grant Number:	NA
ject Status:	Subproject has been	closed. FDU close-out in progre	SS.	
ject Name:	Overhead Signage	Improvements	Project Sponsor/Client:	Aviation
ject Type:	6001 - Landside Fac	ility Improvements	Total Project Estimate:	\$253,000
A Number:	L3140	DOA PM: Dale Thompson	PWD PM: Rober	rt Pirtle
J Number:	4910-8107-3140	Sub-project ID: 6001.061	Grant Number:	NA
ject Status:	Project is complete,	and project closeout is in progress	S	
ject Name:	Remain Over Night	Apron, Phase 1	Project Sponsor/Client:	Aviation
ject Type:	6000 - Airside Improv	vements	Total Project Estimate:	\$9,830,001
A Number:	A3127	DOA PM: Dale Thompson	PWD PM: Tony	Krauss
J Number:	4910-8107-3127	Sub-project ID: 6000.044	Grant Number:	45, 48, 49
ject Status:	Project is complete.	Project close-out in progress.		
ject Name:	Security System Im	provements	Project Sponsor/Client:	Aviation
ject Type:	6501 - Other Improve	ements	Total Project Estimate:	\$2,435,000
A Number:	T3052	DOA PM: Ben Avila	PWD PM: Alison	Von Stein
J Number:	4910-8107-3052	Sub-project ID: 6501.004	Grant Number:	NA
ect Status:	Subproject and FDU	close-out in progress.		
ject Name:	Terminal Trash Chu	ites Improvements	Project Sponsor/Client:	Aviation
ect Type:	5415 - Terminal Impr	ovements	Total Project Estimate:	\$100,000
	T2450	DOA PM: Ben Avila	PWD PM: Burton	n Jones
A Number:	T3158	DOM I W. DOI / WIII	THE THE DUILLO	
A Number: J Number:	4910-8107-3158	Sub-project ID: 5415.047	Grant Number:	NA

1 - Preliminary

Project Name: Ascend Hangar Facility Development Project Sponsor/Client: Ascend

Project Type:

Tenant/Third Party

Total Project Estimate:

ABIA Number:

F5001.01

DOA PM: Richard Chaney

Sub-project ID:

Project Status: N/C

FAA duct bank design documents provided to ASCEND. Meeting with Ascend on 2/17/2011 to discuss

their agreement status and requested amendments.

Project Name:

Refurbishment of Auntie Anne's

Project Sponsor/Client: Auntie Anne's

Project Type:

Tenant/Third Party

Total Project Estimate:

\$0

\$0

ABIA Number:

F4003.03

DOA PM: Richard Chaney

Sub-project ID:

Project Status:

Scoping of drainage lines to be performed on 30Mar2011.

Project Name:

The Tavern

Project Sponsor/Client: DNC

Project Type:

Tenant/Third Party

Total Project Estimate:

\$0

ABIA Number:

F4005.26

DOA PM: Richard Chaney

Sub-project ID:

Project Status:

Preliminary design phase. No change since last report.

Project Sponsor/Client: Waterloo

Project Name: Project Type:

Waterloo Icehouse 2011 Refurbishment

Total Project Estimate:

\$0

\$0

ABIA Number:

Tenant/Third Party F4018.03

DOA PM: Richard Chaney

Sub-project ID:

Project Status:

Scoping of drainage lines to be performed on 30Mar2011

Project Name:

Wok n Roll Refurbishment

Project Sponsor/Client: Wok n Roll

Project Type:

Tenant/Third Party

Total Project Estimate:

ABIA Number:

F4019.02

DOA PM: Richard Chaney

Sub-project ID:

Project Status:

Scoping of drainage lines to be performed on 30Mar2011

TENANT PROJECTS STATUS REPORT

2 - Design					
Project Name:	AA ATO Revisions			Project Sponsor/Client:	American Airlines
Project Type:	Tenant/Third Party			Total Project Estimate:	\$0
ABIA Number:	F1002.09	DOA PM:	Richard Chaney	Sub-project ID:	
Project Status:	Received 100% CD's	on 2/24/201	1, no change		
Project Name:	HDS RNA/NGSI Aus	tin Article		Project Sponsor/Client:	HDS RNA/NGSI
Project Type:	Tenant/Third Party			Total Project Estimate:	\$50,000
ABIA Number:	F4008.08	DOA PM:	Richard Cahney	Sub-project ID:	
Project Status:	Received first design	submittal			
Project Name:	HDS RNA/NGSI Virg	in/Ruta May	a Coffee	Project Sponsor/Client:	HDS RNA/NGSI
Project Type:	Tenant/Third Party			Total Project Estimate:	\$300,000
ABIA Number:	F4008.07	DOA PM:	Richard Chaney	Sub-project ID:	
Project Status:	First Designsubmittall	received			

TENANT PROJECTS STATUS REPORT

4 - Construction

Project Name: **ACE Signage** Project Sponsor/Client: ACE

Project Type:

Tenant/Third Party

Total Project Estimate:

ABIA Number:

F8001.02

DOA PM: Richard Chaney

Sub-project ID:

Project Status:

No change since last report.

Project Name:

Armed Forces Reserve Center & Vehicle

Project Sponsor/Client: AFRC VMF

\$0

Project Type:

Tenant/Third Party

Maintenance Facility

Total Project Estimate:

\$41,500,000

ABIA Number:

F6005.02

DOA PM: Richard Chaney

Sub-project ID:

Project Status:

Site work in progress. Project moving forward without any major issues.

Project Name:

Clean Energy Facility

Project Sponsor/Client: CNG

Total Project Estimate:

\$1,500,000

Project Type: ABIA Number: Tenant/Third Party

F7034.01

DOA PM: Richard Chaney

Sub-project ID:

Project Status:

Project on schedule. Signage installed on 71-E access road, signage is installed incorrectly and will

have to be redone. Canopy installed.

TENANT PROJECTS STATUS REPORT

7 - Post-construction


Project Name: ABIA Utility Use Improvements Project Sponsor/Client: Shane Harbinson

Project Type: COA Third Party Total Project Estimate: \$1,800,000

ABIA Number: U6000 DOA PM: Ben Avila Sub-project ID: NA

Project Status: Requested measurement and verification documents as a part of post-construction documentation

AUSTIN PASSENGER TRAFFIC FISCAL YEAR 2011 vs 2010

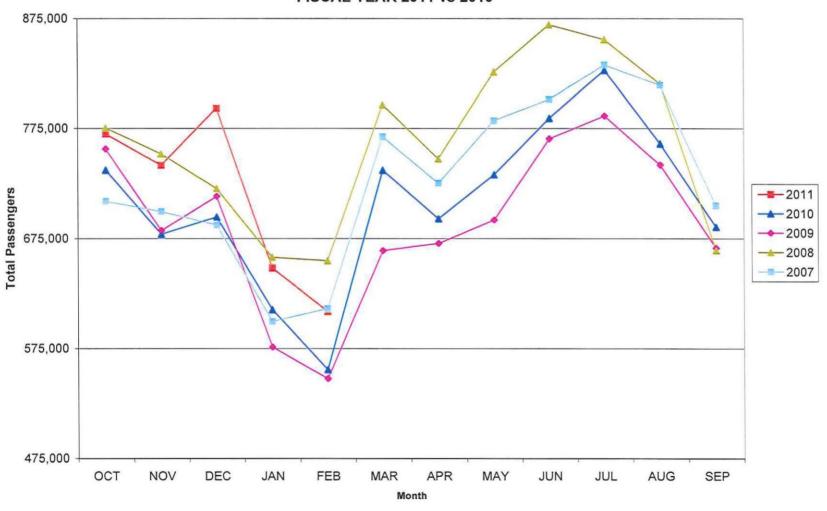

Austin-Bergstrom International Airport

Aviation Activity Report Fiscal Year 2011 vs 2010

	02/2011	02/2010	Percent Change	10/2010 - 02/2011	10/2009 - 02/2010	Percent Change
Passenger Activity						
Domestic Enplaned Revenue	295,155	268,260	10.03	1,760,360	1,596,698	10.25
Domestic Deplaned Revenue	296,120	271,069	9.24	1,714,729	1,590,020	7.84
International Enplaned Revenue	112	0	0.00	112	0	0.00
International Deplaned Revenue	154	0	0.00	154	0	0.00
Domestic Enplaned Non-Revenue	8,597	8,525	0.84	45,225	46,084	-1.86
Domestic Deplaned Non-Revenue	8,292	7,953	4.26	42,614	42,818	-0.48
International Enplaned Non-Revenue	7	0	0.00	7	0	0.00
International Deplaned Non-Revenue	0	0	0.00	0	0	0.00
South Terminal-Intl Enplaned Revenue	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Revenue	0	0	0.00	0	0	0.00
South Terminal-Intl Enplaned Non-Revenue	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Non-Revenue	0	0	0.00	0	0	0.00
Passenger Totals	608,437	555,807	9.47	3,563,201	3,275,620	8.78

CURRENT PASSENGER RECORD = 869,308

RECORD SET = JUNE 2008

rcraft Operations	2724F024	13113410		(PUIS-NAISEN)		700.742.02
Air Carrier	7,056	6,610	6.75	38,393	36,929	3.96
Commuter & Air Taxi	1,354	1,482	-8.64	7,758	7,298	6.30
Military	625	599	4.34	2,785	2,839	-1.90
General Aviation						
Itinerant	4,040	4,005	0.87	23,660	22,019	7.45
Local	192	174	10.34	1,221	1,128	8.24
Total G.A.	4,232	4,179	1.27	24,881	23,147	7.49
Total Operations	13,267	12,870	3.08	73,817	70,213	5.13

Austin-Bergstrom International Airport


Aviation Activity Report Fiscal Year 2011 vs 2010

	02/2011	02/2010	Percent Change	10/2010 - 02/2011	10/2009 - 02/2010	Percent Change
Cargo Activity						
Mail						
Domestic Enplaned Mail	218,498	237,587	-8.03	982,369	1,077,401	-8.82
Domestic Deplaned Mail	250,639	294,903	-15.01	1,391,591	1,718,852	-19.04
International Enplaned Mail	0	0	0.00	0	0	0.00
International Deplaned Mail	0	0	0.00	0	0	0.00
South Terminal-Intl Enplaned Mail	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Mail	0	0	0.00	0	0	0.00
Mail Totals	469,137	532,490	-11.90	2,373,960	2,796,253	-15.10
Cargo						
Domestic Enplaned Cargo	4,936,510	4,795,407	2.94	25,279,375	28,938,123	-12.64
Domestic Deplaned Cargo	4,771,194	4,778,809	-0.16	25,807,831	25,129,166	2.70
International Enplaned Cargo	307,466	260,442	18.06	1,674,132	1,840,414	-9.04
International Deplaned Cargo	540,099	443,454	21.79	1,779,139	823,841	115.96
South Terminal-Intl Enplaned Cargo	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Cargo	0	0	0.00	0	0	0.00
Cargo Totals	10,555,269	10,278,112	2.70	54,540,477	56,731,544	-3.86
Belly Freight						
Domestic Enplaned Belly Freight	415,540	478,995	-13.25	2,598,423	3,373,282	-22.97
Domestic Deplaned Belly Freight	489,951	470,408	4.15	2,459,056	2,537,997	-3.11
International Enplaned Belly Freight	0	0	0.00	0	0	0.00
International Deplaned Belly Freight	0	0	0.00	0	0	0.00
South Terminal-Intl Enplaned Belly Frt	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Belly Frt	0	0	0.00	0	0	0.00
Belly Freight Totals	905,491	949,403	-4.63	5,057,479	5,911,279	-14.44
Cargo Totals (Mail, Cargo, Belly Freight)	11,929,897	11,760,005	1.44	61,971,916	65,439,076	-5.30

CURRENT CARGO RECORD = 40,215,518

RECORD SET = MARCH 2001

AUSTIN PASSENGER TRAFFIC Calendar Year 2011 vs 2010

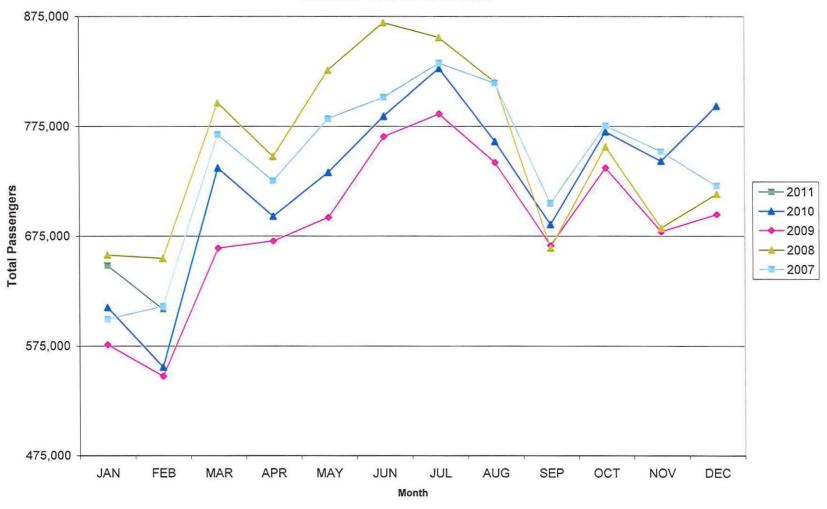

Austin-Bergstrom International Airport

Aviation Activity Report Calendar Year 2011 vs 2010

	02/2011	02/2010	Percent Change	01/2011 - 02/2011	01/2010 - 02/2010	Percent Change
Passenger Activity						
Domestic Enplaned Revenue	295,155	268,260	10.03	605,965	561,819	7.86
Domestic Deplaned Revenue	296,120	271,069	9.24	615,279	569,365	8.06
International Enplaned Revenue	112	0	0.00	112	0	0.00
International Deplaned Revenue	154	0	0.00	154	0	0.00
Domestic Enplaned Non-Revenue	8,597	8,525	0.84	18,054	18,019	0.19
Domestic Deplaned Non-Revenue	8,292	7,953	4.26	17,027	16,630	2.39
International Enplaned Non-Revenue	7	0	0.00	7	0	0.00
International Deplaned Non-Revenue	0	0	0.00	0	0	0.00
South Terminal-Intl Enplaned Revenue	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Revenue	0	0	0.00	0	0	0.00
South Terminal-Intl Enplaned Non-Revenue	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Non-Revenue	0	0	0.00	0	0	0.00
Passenger Totals	608,437	555,807	9.47	1,256,598	1,165,833	7.79

CURRENT PASSENGER RECORD = 869,308

RECORD SET = JUNE 2008

Aircraft Operations						
Air Carrier	7,056	6,610	6.75	14,851	14,052	5.69
Commuter & Air Taxi	1,354	1,482	-8.64	2,790	2,848	-2.04
Military	625	599	4.34	1,261	1,340	-5.90
General Aviation						
Itinerant	4,040	4,005	0.87	8,440	8,176	3.23
Local	192	174	10.34	489	558	-12.37
Total G.A.	4,232	4,179	1.27	8,929	8,734	2.23
Total Operations	13,267	12,870	3.08	27,831	26,974	3.18

Austin-Bergstrom International Airport

Aviation Activity Report Calendar Year 2011 vs 2010

	02/2011	02/2010	Percent Change	01/2011 - 02/2011	01/2010 - 02/2010	Percent Change
Cargo Activity						
Mail						
Domestic Enplaned Mail	218,498	237,587	-8.03	376,134	475,380	-20.88
Domestic Deplaned Mail	250,639	294,903	-15.01	557,908	678,094	-17.72
International Enplaned Mail	0	0	0.00	0	0	0.00
International Deplaned Mail	0	0	0.00	0	0	0.00
South Terminal-Intl Enplaned Mail	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Mail	0	0	0.00	0	0	0.00
Mail Totals	469,137	532,490	-11.90	934,042	1,153,474	-19.02
Cargo						
Domestic Enplaned Cargo	4,936,510	4,795,407	2.94	9,746,333	9,881,217	-1.37
Domestic Deplaned Cargo	4,771,194	4,778,809	-0.16	9,692,583	9,818,505	-1.28
International Enplaned Cargo	307,466	260,442	18.06	522,503	483,844	7.99
International Deplaned Cargo	540,099	443,454	21.79	784,158	823,841	-4.82
South Terminal-Intl Enplaned Cargo	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Cargo	0	0	0.00	0	0	0.00
Cargo Totals	10,555,269	10,278,112	2.70	20,745,577	21,007,407	-1.25
Belly Freight						
Domestic Enplaned Belly Freight	415,540	478,995	-13.25	945,587	1,172,202	-19.33
Domestic Deplaned Belly Freight	489,951	470,408	4.15	993,316	1,000,951	-0.76
International Enplaned Belly Freight	0	0	0.00	0	0	0.00
International Deplaned Belly Freight	0	0	0.00	0	0	0.00
South Terminal-Intl Enplaned Belly Frt	0	0	0.00	0	0	0.00
South Terminal-Intl Deplaned Belly Frt	0	0	0.00	0	0	0.00
Belly Freight Totals	905,491	949,403	-4.63	1,938,903	2,173,153	-10.78
Cargo Totals (Mail, Cargo, Belly Freight)	11,929,897	11,760,005	1.44	23,618,522	24,334,034	-2.94

CURRENT CARGO RECORD = 40,215,518

RECORD SET = MARCH 2001

CITY OF AUSTIN

AUSTIN-BERGSTROM INTERNATIONAL AIRPORT

Airport Operating Fund 5070

Income Statement - For Internal Use Only Fiscal Year to Date for 5 Months ended February 28, 2011

	Amended Budget	Budget Annualized 5 Months	Year to Date w/ Encumb	Y-T-D Variance Fav (Unfav)	Y-T-D % Variance Fav (Unfav)
REVENUE					
AIRLINE REVENUE Landing Fees Terminal Rental & Other Fees TOTAL AIRLINE REVENUE	20,400,000 19,964,000 40,364,000	8,500,000 8,318,333 16,818,333	7,488,108 8,506,998 15,995,106	(1,011,892) 188,665 (823,227)	(11.9%) 2.3% (4.9%)
NON-AIRLINE REVENUE					
Parking	25,903,000	10,792,917	10,637,520	(155, 397)	(1.4%)
Other Concessions	16,545,000	6,893,750	6,328,087	(565,663)	(8.2%)
Other Rentals and Fees TOTAL NON-AIRLINE REVENUE	<u>6,644,000</u> 49,092,000	2,768,333	2,657,508 19,623,115	(110,825) (831,885)	(4.0%)
TOTAL NON-AIRLINE REVENUE	49,092,000	20,455,000	19,023,113	(031,003)	(4.170)
Interest Income	450,000	187,500	94,309	(93, 191)	(49.7%)
TOTAL REVENUE	89,906,000	37,460,833	35,712,530	(1,748,303)	(4.7%)
OPERATING REQUIREMENTS					
Fac Mgmt, Ops and Airport Security	34,273,931	14,281,947	14,053,799	228,148	1.6%
Airport Planning and Development Support Services	1,514,217 11,085,613	630,974 4,619,375	677,891 3,760,724	(46,917) 858,651	(7.4%) 18.6%
Business Services	11,104,575	4,627,276	3,653,054	974,222	21.1%
TOTAL OPERATING EXPENSES	57,978,336	24,159,572	22,145,468	2,014,104	8.3%
Debt Service	20.404	10.540	15.050	(2 507)	(20.00()
GO Debt Service Fund 2003 Series Airport Revenue Bond DS	30,101 4,525,750	12,543 1,885,880	15,050 1,883,000	(2, 507) 2,880	(20.0%) 0.2%
2005 Variable rate Notes (Swap)	27,067,376	11,278,976	9,351,778	1,927,198	17.1%
2005 Variable rate Notes Fees	1,773,275	738,924	922,886	(183,962)	(24.9%)
\$28 Million Variable Rate Note	741,041	308,792	30,394	278,398	90.2%
PFC Debt Service Funding	(14,009,330)	(5,837,688)	(5,405,240)	(432,448)	7.4%
TOTAL Net Debt Service	20,128,213	8,387,427	6,797,868	1,589,559	19.0%
OTHER REQUIREMENTS					
Workers' Compensation	333,827	139,106	139,094	12	0.0%
Citywide Adminstrative Support	1,697,020	707,148	707,092	56	0.0%
Communications & Technology Mgmt	1,465,059 104,000	610,490 43,337	610,443	47 4	0.0% 0.0%
Accrued Payroll Additional Retirement Contribution	934,242	389,299	43,333 370,771	18,528	4.8%
Compensation Adjustment	22,425	9,344	3,918	5,426	58.1%
Liability Reserve	23,000	9,584	9,581	3	0.0%
Operating Reserve	686,000	285,856	0	285,856	100.0%
CTECC	57,161	23,819	23,820	(1)	(0.0%)
Trunked Radio Allocation	112,874	47,035	47,032	3	0.0%
TOTAL OTHER REQUIREMENTS	5,435,608	2,265,018	1,955,084	309,934	13.7%
TOTAL REQUIREMENTS	83,542,157	34,812,017	30,898,420	3,913,597	11.2%
EXCESS (DEFICIT) OF TOTAL AVAILABLE FUNDS OVER					
TOTAL REQUIREMENTS	6,363,843	2,648,816	4,814,110	2,165,294	81.7%

CITY OF AUSTIN AUSTIN-BERGSTROM INTERNATIONAL AIRPORT **FUND SUMMARY COMPARISON**

This month - This Year vs. Last Year FY11 (Feb 11) vs FY10 (Feb 10)

Fiscal YTD - This Year vs. Last Year FY11 (Oct 10 - Feb 11) vs FY10 (Oct 09 - Feb 10)

<u></u>		. (
Airline Revenue	FY11 Feb-11	FY10 Feb-10	Fav (Unfav) § Variance	Fav (Unfav) % Variance	FY11 YTD Feb-11	FY10 YTD Feb-10	Fav (Unfav) § Variance	Fav (Unfav) % Variance
Landing Fees	1,391,932	1,280,878	111,054	8.7%	7,488,108	7,232,401	255,707	3.5%
Terminal Rental & Other Fees	1,734,930	1,584,870	150,060	9.5%	8,506,998	7,942,366	564,632	7.1%
Total Airline Revenue	3,126,862	2,865,748	261,114	9.1%	15,995,106	15,174,767	820,339	5.4%
Non-Airline Revenue								
Parking	1,870,106	1,797,674	72,432	4.0%	10,637,520	9,931,899	705,621	7.1%
Food/Beverage & Retail	386,106	383,487	2,619	0.7%	2,131,089	1,991,095	139,994	7.0%
Rental Car	691,169	778,649	(87,480)	(11.2%)	3,728,082	3,603,119	124,963	3.5%
Advertising	45,834	8,391	37,443	446.2%	150,629	47,955	102,674	214.1%
Ads Barter Revenue	2,285	3,125	(840)	(26.9%)	13,945	19,050	(5,105)	(26.8%)
Other Concessions	60.051	41,029	19,022	46.4%	304,342	264,324	40,018	15.1%
Other Rentals and Fees *	519,412	492,602	26,810	5.4%	2,657,508	2,625,711	31,797	1.2%
Total Non-Airline Revenue	3,574,963	3,504,957	70,006	2.0%	19,623,115	18,483,153	1,139,962	6.2%
Interest Income	9,093	36,467	(27,374)	(75 1%)	94,309	194,628	(100,319)	(51.5%)
Total Operating Revenue	6,710,918	6,407,172	303,746	4.7%	35,712,530	33,852,548	1,859,982	5.5%
=								
Operating Requirements								
Fac Mgmt, Ops and Airport Security **	2,713,468	2,560,239	(153,229)	(6.0%)	14,053,799	13,509,009	(544,790)	(4.0%)
Airport Planning and Development **	111,969	135,919	23,950	17.6%	677,891	581,243	(96,648)	(16.6%)
Support Services **	619,850	840,184	220,334	26.2%	3,760,724	3,672,493	(88,231)	(2.4%)
Business Services **	711,273	621,384	(89,889)	(14.5%)	3,653,054	3,434,674	(218,380)	(6.4%)
Total Operating Expense	4,156,560	4,157,726	1,166	0.0%	22,145,468	21,197,419	(948,049)	(4.5%)
Debt Service								
GO Debt Service Fund	0	0	0	N/A	15,050	14,259	(791)	(5.5%)
2003 Series Airport Revenue Bond DS	377,000	376,000	(1,000)	(0.3%)	1,883,000	1,878,000	(5,000)	(0.3%)
2005 Variable rate Notes (Swap)	1,871,350	1,852,482	(18,868)	(1.0%)	9,351,778	9,328,250	(23,528)	(0.3%)
2005 Variable rate Notes Fees	0	9,274	9,274	100.0%	922,886	976,180	53,294	5.5%
\$28 Million Variable Rate Note	5,531	4,349	(1,182)	(27.2%)	30.394	27,386	(3,008)	(11.0%)
PFC Debt Service Funding	(1,001,005)	(989,083)	11,922	(1.2%)	(5,405,240)		25,775	(0.5%)
Total Debt Service	1,252,876	1,253,022	146	0.0%	6,797,868		46,742	0.7%
Other Beauty ments								
Other Requirements Workers' Compensation	27,819	26,682	(1,137)	(4.3%)	139,094	133,406	(5,688)	(4 3%)
Citywide Administrative Support	141,419	141,505	86	0.1%	707,092		433	0.1%
Communications & Technology Mgmt	122,088	101,096	(20,992)	(20.8%)	610,443		(104,960)	(20.8%)
Accrued Payroll	8,670	7,250	(1,420)	(19.6%)	43,333		(7,083)	(19.5%)
Additional Retirement Contribution	71,453	53,081	(18,372)	(34.6%)	370,771	265,404	(105,367)	(39.7%)
Compensation Adjustment	724	255	(469)	(183.9%)	3.918		(1,332)	(51.5%)
CTECC	4,763	0	(4,763)	-1-017	23,820		(23,820)	N/A
Trunked Radio Allocation	9,406	8,654	(752)		47,032		(3,763)	(8.7%)
			12				(3,763)	
Liability Reserve	1,917	1,916	(1)		9,581	9,583		0.0%
Total Other Requirements	388,259	340,439	(47,820)	(14.0%)	1,955,084		(251,578)	(14.8%)
Total Requirements	5,797,695	5,751,187	(46,508)	(0.8%)	30,898,420	29,745,535	(1,152,885)	(3.9%)
011001110 (0551017) 25 70711 21411 1215								
SURPLUS (DEFICIT) OF TOTAL AVAILABLE FUNDS OVER TOTAL REQUIREMENTS	\$ 913,223 \$	655,985	\$ 257,238	39.2%	\$ 4,814,110	\$ 4,107,013	\$ 707.097	17.2%
		200,030			1	.,,		

^{*} FY 2010 STS, Bldg Maint, and Fac Svcs expense refunds are stated as revenue to be consistent with FY 2011 ** FY 2010 Operating Requirements recategorized to be consistent with FY 2011

CITY OF AUSTIN AUSTIN-BERGSTROM INTERNATIONAL AIRPORT Non-Airline Revenue Detail

This month - This Year vs. Last Year FY11 (Feb 11) vs FY10 (Feb 10)

Fiscal YTD - This Year vs. Last Year FY11 (Oct 10 - Feb 11) vs FY10 (Oct 09 - Feb 10)

	February 2011	February 2010	Fav (Unfav) Variance	Fav (Unfav) %	YTD FY11	YTD FY10	Fav (Unfav) Variance	Fav (Unfav) %
PARKING REVENUES								
Parking	1,793,458	1,736,217	57,241	3.30%	10,218,251	9,590,334	627,917	6.55%
Off Airport Parking	76,648	61,457	15,191	24.72%	419,269	341,565	77,704	22.75%
TOTAL PARKING REVENUES	1,870,106	1,797,674	72,432	4.03%	10,637,520	9,931,899	705,621	7.10%
OTHER CONCESSIONS								
Rental Cars	691,169	778,649	(87,480)	(11.23%)	3,728,082	3,603,119	124,963	3.47%
Food and Beverage	233,454	201,723	31,731	15.73%	1,236,092	1,069,063	167,029	15.62%
Advertising	45,834	8,391	37,443	446.23%	150,629	47,955	102,674	214.10%
Telephone	29,818	12,753	17,065	133.81%	148,871	115,772	33,099	28.59%
News and Gift	152,652	181,764	(29,112)	(16.02%)	894,997	922,032	(27,035)	(2.93%)
Ads Barter Revenue	2,285	3,125	(840)	(26.88%)	13,945	19,050	(5,105)	(26.80%)
Airline Catering	12,633	12,084	549	4.54%	66,638	67,643	(1,005)	(1.49%)
Vending Commissions	17,288	15,937	1,351	8.48%	87,399	79,633	7,767	9.75%
Miscellaneous	312	255	57	22.35%	1,434	1,276	158	12.38%
TOTAL OTHER CONCESSIONS	1,185,445	1,214,681	(29,236)	(2.41%)	6,328,087	5,925,543	402,544	6.79%
OTHER RENTALS & FEES	official and a	Carried Chalanters in	Service	Nach Mediate	DA SALHous STEEL 1	194355-19470	Westile	-3137448
Building-FBOs	41,316	40,934	382	0.93%	206,579	200,619	5,960	2.97%
Building - Other	103,514	107,752	(4,238)	(3.93%)	540,381	534,482	5,899	1.10%
Ground Rent	71,239	70,986	253	0.36%	356,206	370,229	(14,023)	(3.79%)
Telephone - STS	31,746	53,470 *	(21,724)	(40.63%)	174,031	221,376 *	(47,345)	(21.39%)
Building Maintenance Reimbursements	7,719	7,730 -	(11)	(0.14%)	47,835	47,822 *	13	0.03%
Facility Services Reimbursements	4,075	4,313 *	(238)	(5.52%)	20,377	23,183 *	(2,806)	(12.10%)
Hotel	37,438	-6,111	43,549	(712.63%)	189,431	112,390	77,041	68.55%
GTSA Shuttle Permits	600	725	(125)	(17.24%)	11,630	20,775	(9,145)	(44.02%)
Taxi-Cab	17,987	23,381	(5,394)	(23.07%)	96,330	126,021	(29,691)	(23,56%)
Cargo Facilities	16,996	16,798	198	1.18%	84,979	83,992	987	1.18%
Fuel Flowage	40,167	32,441	7,726	23.82%	245,332	221,545	23,787	10.74%
Fuel Facility Fees	62,219	62,218	1	0.00%	311,095	309,844	1,251	0.40%
Cargo Ramp Use Fee	36,326	46,725	(10,399)	(22.26%)	181,964	221,961	(39,997)	(18.02%)
Other	23,966	22,270	1,696	7.62%	130,953	90,574	40,379	44.58%
Cash Over/Short	754	653	101	15.47%	3,849	3,654	195	5.34%
GSEM User Fee	3,177	3,177	0	0.00%	15,885	15,885	0	0.00%
Airport ID Badges, Fingerprints, Keys	4,362	5,140	(778)	(15.14%)	24,840	21,359	3,481	16.30%
Top Caps	0	0	0	N/A	0	0	0	N/A
Sale of Plans and Specs	0	0	0	N/A	0	0	0	N/A
TOTAL OTHER RENTALS & FEES	519,412	492,602	26,810	5.44%	2,657,508	2,625,711	31,797	1.21%
TOTAL NON-AIRLINE REVENUE	3,574,963	3,504,957	70,006	2.00%	19,623,115	18,483,153	1,139,962	6.17%
ACTUAL % OF TOTAL REVENUE	53.3%	54.7%	(1.4)	(2.56%)	54.9%	54.6%	0.3	0.55%
TARGET %	60.0%				60.0%			

^{*} FY 2010 STS, Bldg Maint, and Fac Svcs expense refunds are stated as revenue to be consistent with FY 2011

CITY OF AUSTIN AUSTIN-BERGSTROM INTERNATIONAL AIRPORT NON-AIRLINE REVENUE ACTUALS

This month - This Year vs. Last Year FY11 (Feb 11) vs FY10 (Feb 10)

Fiscal YTD - This Year vs. Last Year

0

FY11 Feb-11	FY10 Feb-10	Fav (Unfav) § Variance	Fav (Unfav) % Variance	FY11 YTD Feb-11	FY10 YTD Feb-10	Fav (Unfav) \$ Variance	Fav (Unfav) % Variance
762,493	717,447	45,046	6.3%	3,783,722	3,562,544	221,178	6.2%
228,411	187,840	40,571	21.6%	1,215,017	1,041,488	173,529	16.7%
163,842	169,925	(6,083)	(3.6%)	898,953	916,480	(17,527)	(1,9%)
1,154,746	1,075,212	79,534	7.4%	5,897,692	5,520,511	377,180	6.8%
32,143	30,640	1,503	4.9%	166,108	160,853	5,256	3.3%
32,143	30,640	1,503	4.9%	166,108	160,853	5,256	3.3%
	762,493 228,411 163,842 1,154,746	Feb-11 Feb-10 762,493 717,447 228,411 187,840 163,842 169,925 1,154,746 1,075,212 32,143 30,640	Feb-11 Feb-10 \$ Variance 762,493 717,447 45,046 228,411 187,840 40,571 163,842 169,925 (6,083) 1,154,746 1,075,212 79,534 32,143 30,640 1,503	Feb-11 Feb-10 \$ Variance % Variance 762,493 717,447 45,046 6.3% 228,411 187,840 40,571 21.6% 163,842 169,925 (6,083) (3.6%) 1,154,746 1,075,212 79,534 7.4% 32,143 30,640 1,503 4.9%	FY11 FY10 Fav (Unfav) \$ Variance Fav (Unfav) % Variance YTD Feb-11 762,493 717,447 45,046 6.3% 3,783,722 228,411 187,840 40,571 21.6% 1,215,017 163,842 169,925 (6,083) (3.6%) 898,953 1,154,746 1,075,212 79,534 7.4% 5,897,692 32,143 30,640 1,503 4.9% 166,108	FY11 Feb-11 FY10 Feb-10 Fav (Unfav) § Variance Fav (Unfav) % Variance YTD Feb-11 YTD Feb-10 762,493 717,447 45,046 6.3% 3,783,722 3,562,544 228,411 187,840 40,571 21.6% 1,215,017 1,041,488 163,842 169,925 (6,083) (3.6%) 898,953 916,480 1,154,746 1,075,212 79,534 7.4% 5,897,692 5,520,511 32,143 30,640 1,503 4.9% 166,108 160,853	FY11 Feb-11 FY10 Feb-10 Fav (Unfav) § Variance Fav (Unfav) % Variance YTD Feb-11 YTD Feb-10 Fav (Unfav) § Variance 762,493 717,447 45,046 6.3% 3,783,722 3,562,544 221,178 228,411 187,840 40,571 21.6% 1,215,017 1,041,488 173,529 163,842 169,925 (6,083) (3.6%) 898,953 916,480 (17,527) 1,154,746 1,075,212 79,534 7.4% 5,897,692 5,520,511 377,180 32,143 30,640 1,503 4.9% 166,108 160,853 5,256

AUSTIN-BERGSTROM INTERNATIONAL AIRPORT ENPLANEMENTS FY 2010 VS. FY 2011

	FY 2011	FY 2010	Month over Month Change %	YTD Change %
October	381,906	366,747	4.13%	4.13%
November	372,492	343,369	8.48%	6.24%
December	427,168	353,737	20.76%	11.06%
January	320,267	303,053	5.68%	9.87%
February	303,871	276,785	9.79%	9.86%
March	##	363,280		
April	35	351,621		
May	: ₩	369,844		
June	22	398,910		
July		417,893		
August	3 7 8	369,542		
September	-	342,934		
	1,805,704	4,257,715		


CITY OF AUSTIN AUSTIN-BERGSTROM INTERNATIONAL AIRPORT ADVERTISING CONTRACT ANALYSIS


This month - This Year vs. Last Year FY11 (Feb 11) vs FY10 (Feb 10)

Fiscal YTD - This Year vs. Last Year FY11 (Oct 10 - Feb 11) vs FY10 (Oct 09 - Feb 10)

Advertising	FY11 <u>Feb-11</u>	FY10 Feb-10	Fav (Unfav) \$ Variance	Fav (Unfav) % Variance	FY11 YTD Feb-11	FY10 YTD Feb-10	Fav (Unfav) \$ Variance	Fav (Unfav) % Variance
Hotel	1,834	4,597	(2,763)	(60.1%)	17,853	22,985	(5,132)	(22.3%)
Cab	585	344	241	70.1%	1,961	1,720	241	14.0%
Others:								
1st Commercial Credit	572	0	572	N/A	572	0	572	N/A
Barracuda Networks	1,042	0	1,042	N/A	1,042	0	1,042	N/A
Fast Company	1,375	0	1,375	N/A	1,375	0	1,375	N/A
Google	15,425	0	15,425	N/A	15,425	0	15,425	N/A
Southwest Airlines	5,893	0	5,893	N/A	46,693	0	46,693	N/A
Gemalto	779	3,300	(2,521)	(76.4%)	7,379	16,500	(9,121)	(55.3%)
KVUE	681	0	681	N/A	681	0	681	N/A
Roger Beasley Import Group	2,145	0	2,145	N/A	2,145	0	2,145	N/A
The University ofTexas Arlington	395	0	395	N/A	395	0	395	N/A
The University ofTexas Austin	859	0	859	N/A	859	0	859	N/A
St. David's Medical Group	3,547	0	3,547	N/A	43,547	0	43,547	N/A
Oakland International Airport	0	0	0	N/A	0	6,000	(6,000)	(100.0%)
Heather McMahan Art	0	150	(150)	(100.0%)	0	750	(750)	(100.0%)
Minimum Annual Guarantee	10,702	0	10,702	N/A	10,702	0	10,702	N/A
TOTAL	45,834	8,391	37,443	446.2%	150,629	47,955	102,674	214.1%

GROUND TRANSPORTATION TRANSACTIONS MARCH 2011

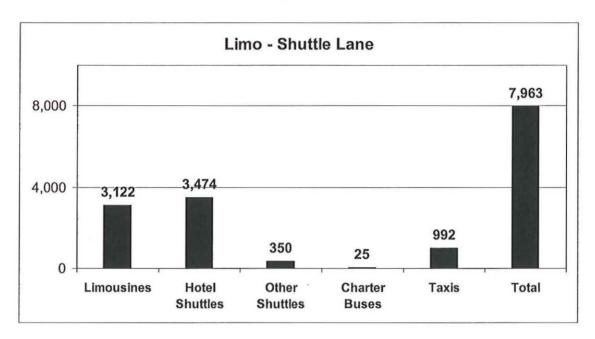

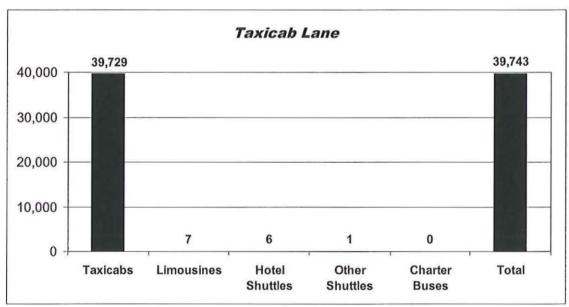

YEAR TO	YEAR COMPARISON	
SERVICE CATEGORY	MARCH 2011	MARCH 2010
TAXICAB	40,721	32,042
LIMOUSINE	3,129	2,143
HOTEL SHUTTLE	3,480	3,084
OTHER SHUTTLE	351	410
CHARTER BUS	25	7
OVERALL TOTAL	47,706	37,686



RCA - Purchasing	Austin City Council	Item ID:	5329
Meeting Date:	April 21, 2011		
Department:	Purchasing		

Subject

Authorize award and execution of a contract through the Houston Galveston Area Council of Governments Cooperative Purchasing Program (HGAC) with NATIONAL BUS SALES AND LEASING, INC., Marietta, GA, for the purchase of eleven passenger buses in an amount not to exceed \$1,097,297.60.

Amount and Source of Funding

Funding is available in the Fiscal Year 2010-2011 Operating Budget of the Aviation Department.

Fiscal Note

There is no unanticipated fiscal impact. A fiscal note is not required.

Purchasing Language:	Cooperative Purchase.
Prior Council Action:	
For More Information:	Sharon Patterson, Senior Buyer/972-4014
Boards and Commission Action:	
MBE / WBE:	This cooperative purchase is exempt from the MBE/WBE Ordinance. This exemption is in compliance with Chapter 2-9D of the City Code (Minority-Owned and Women-Owned Business Enterprise Procurement Program). No subcontracting opportunities were identified; therefore, no goals were established for this contract.
Related Items:	

Additional Backup Information

This contract is for the purchase of 11 new passenger shuttle buses to be assigned to the Aviation Department.

Prior to October 2009, the company who was under contract to manage the parking operations at Austin Bergstrom International Airport (ABIA) was responsible for the purchase of all passenger shuttle buses used at the airport. These buses were then amortized and reimbursed by the City over the term of the contract. Under the terms of the new contract that began in October 2009, the City assumed responsibility for the purchase of the shuttle buses.

The Austin Climate Protection team and Fleet have worked together to develop a vehicle purchasing process in our progress towards our citywide objective of obtaining carbon neutrality by 2020. The development of the purchasing criteria incorporates emissions impact, available technologies on the market, physical demands on the vehicle, and service application. These criteria are applied to all vehicles submitted to Fleetfor purchase.

All of these buses are powered with engines capable of burningCompressed Natural Gas (CNG) fuel. In line with Austin Climate Protection Program goals, CNG provides an approximate 25% reduction in greenhouse gas emissions

versus using gasoline and an approximate 25% reduction versus using diesel.

The buses in this RCA have been recommended for purchase utilizing a process that involves the Fleet Officer, affected Department Directors, and Assistant City Managers (ACMs). ACM approval is rquired for all new additions to the City's fleet prior to any requests made to the Purchasing Office.

Five of the buses will be able to transport 14 passengers, four of the buses will be able to transport 25 passengers, and two of the buses will be equipped with a wheelchair lift and will be able to transport 18-20 passengers. All the busses will be equipped with a luggage rack.

The Purchasing Office conducted an analysis to determine that the National Bus Sales and Leasing, Inc. HGAC contract is the best value to the City. This contract offered the lowest prices and is able to provide buses that fully meet the needs of the using department. National Bus Sales and Leasing, Inc. is contracted through HGAC to supply these types of buses to other public entities statewide as a result of a competitive bidding process. Utilizing the HGAC contract provides for volume discount pricing as well as the earliest opportunity to place the City's bus order.

V	4 S 1 N 6 I	1 5 (()	
	A G	ENDA	
RCA	Austin City Council	Item ID	5158
Meeting Date:	4/21/2011	Department:	Aviation
		Subject	
Approve an ordinance a from operation of the fa		de to require that a heli-faci	lity maintain insurance for claims arising

Amount and Source of Funding

Fiscal Note

There is no unanticipated fiscal impact. A fiscal note is not required.

Purchasing Language:		
Prior Council Action:		
For More Information:	Susana Gonzalez, Assistant City Attorney, 530-6364	
Boards and Commission Action:		
MBE / WBE:		
Related Items:		

Additional Backup Information

2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18 ·	
19	
20	
21	
22	
23	
24	
25	

26

27

ORDINANCE NO	
---------------------	--

AN ORDINANCE AMENDING SECTION 13-1-184 OF THE CITY CODE TO REQUIRE THAT A HELI-FACILITY MAINTAIN INSURANCE FOR CLAIMS ARISING FROM OPERATION OF THE FACILITY.

BE IT ORDAINED BY THE CITY COUNCIL OF THE CITY OF AUSTIN:

PART 1. Subsection (B) of City Code Section 13-1-184 (*Insurance Required; Termination*) is amended to read:

§ 13-1-184 INSURANCE REQUIRED; TERMINATION.

- (B) A policy under this section shall:
 - (1) name the City as an additional insured;
 - (2) <u>provide coverage against</u> [indemnify the City from] all claims arising out of the operation of the heli-facility, including <u>bodily injury</u>, [noise, nuisance,] personal <u>and advertising</u> injury, death, <u>contractual liability</u>, <u>independent contractors</u>, and property damage;
 - (3) <u>be endorsed to provide the City a thirty (30) day notice of cancellation</u>
 <u>except for non-payment of premium; [not be cancelable before the 30th day after written notice to the director; and]</u>
 - (4) be issued by an insurance company authorized to do business in the State of Texas; and [-]
 - (5) contain waiver of subrogation and recovery in favor of the City.

PART 2. The council waives the requirements of Section 2-5-13 of the City Code for this ordinance.

PART 3. This ordinance takes effect on _________, 2011.

	, 2011	§ § 	Lee Leffingwell Mayor
APPROVED: _	Karen M. Kennard City Attorney	ATTEST: _	Shirley Gentry City Clerk
	8 3		
		্	



Construction Contract CITY OF AUSTIN RECOMMENDATION FOR COUNCIL ACTION

AGENDA DATE: May 12, 2011

PAGE: 1 of 2

<u>SUBJECT:</u> Authorize execution of a construction contract with AUSTIN BRIDGE & ROAD, LP, Austin, TX for the ABIA Remain Over Night (RON) Apron Expansion – Phase 2, in the amount of \$5,290,384 plus a \$529,038 contingency, for a total contract amount not to exceed \$5,819,422.

AMOUNT & SOURCE OF FUNDING: Funding is available in the Fiscal Year 2010-2011 Capital Budget of the Aviation Department.

FISCAL NOTE: A fiscal note is attached.

REQUESTING Public Works
DEPARTMENT:
DIRECTOR'S
AUTHORIZATION:

FOR MORE INFORMATION CONTACT: Robert Pirtle, 974-7234; Dale Thompson, 530-5544; Susan Garnett, 974-7064

PRIOR COUNCIL ACTION: N/A.

BOARD AND COMMISSION ACTION: To be reviewed by the Airport Advisory Commission on April 12, 2011.

PURCHASING: Lowest bid of seven bids received.

MBE / WBE: This contract will be awarded in compliance with the requirements of 49 CFR Part 26 (Disadvantaged Business Enterprise Program) and Chapter 2-9A of the City Code (Minority Owned and Women Owned Business Enterprise Procurement Program) by meeting the goal with 7.44% DBE subcontractor participation.

The City of Austin Department of Aviation (DoA) has determined that additional parking is needed at the terminal apron for aircraft remaining overnight (RON). The proposed location of the RON apron is to the east of, and contiguous to, the existing passenger terminal apron. The RON expansion will accommodate commercial carriers' need for additional overnight aircraft parking in Austin, and will alleviate the need to park aircraft on the terminal apron and taxiways.

The RON apron will be constructed in multiple phases. Construction of the first phase RON apron expansion was completed in the fall of 2010. The RON Phase 2 expansion (this project) will add overnight parking space for an additional nine commercial aircraft. The project includes an extension of the apron trench drain system, adjustments to the water quality structures adjacent to the runway, and additional apron lighting. A contingency of 10% has been included to offset potential additional costs that might accrue due to periodic inaccessibility to the work area by the Contractor when airport operations supersede construction operations.

The contract allows 300 calendar days for completion of this project. The project is located within zip code 78719.

M/WBE Summary

Bid documents were distributed to 20 general contractors. Bids were opened on March 17, 2011. Austin Bridge & Road submitted the lowest of seven bids received:

Austin Bridge & Road, LP, Austin, TX	\$5,290,384
Yantis Company, San Antonio, TX	\$5,459,922
Chasco Constructors, LTD., Round Rock, TX	\$5,981,576
Spawglass Civil Construction, Inc., Houston, TX	\$6,083,255
James Construction Group, Belton, TX	\$6,979,387
Jay Reese Contractors, Inc., Austin, TX	\$6,981,996
Southern Industrial Contractors, LLC, Rayville, LA	\$8,271,986

The contractor's choice of work methodology provides for three areas of subcontracting opportunities which are listed below. Participation goals stated in the solicitation were **5.75 DBE**. Total participation estimated on base bid amount of \$5,290,384.

NON DBE TOTAL – PRIME	\$4,594,832	86.85%
Austin Bridge & Road, L.P.	\$4,594,832	86.85%
DBE TOTAL – SUBCONTRACTORS	\$393,622	7.44%
DBE JAG Trucking, Inc., Georgetown, TX (512) 864-9906	\$129,710	2.45%
DBE Roadway Specialties, Inc., Austin, TX (512) 280-6666	\$158,817	3.00%
DBE Royal Vista, Inc., Liberty Hill, TX (512) 515-6824	\$105,095	1.99%
NON M/WBE TOTAL – SUBCONTRACTORS	\$301,930	5.71%
(NON) F&W Electrical Contractors, Inc., Floresville, TX (830) 393-0083	\$297,730	5.63%
(NON) Highway Technologies, Austin, TX (512) 990-9525	\$4,200	0.08%

The Contractor submitted a DBE Compliance Plan that met the goals of the solicitation and was approved by the Department of Small & Minority Business Resources. Second and third low bidder information is provided.

SECOND BIDDER - Yantis Company, San Antonio, TX \$5,459,922 84.34% NON DBE prime participation; 7.30% DBE; 8.36% Non DBE subcontractor participation.

THIRD BIDDER - Chasco Constructors, LTD., Round Rock, TX \$5,981,576 43.73% NON M/WBE prime participation; 8.01% DBE; 48.26% Non DBE subcontractor participation.

CITY OF AUSTIN RECOMMENDATION FOR COUNCIL ACTIONPAGE 1 OF 2 VENDOR NAME: ALLIED ELECTRONICS, INC.

SUBJECT: Authorize award and execution of Amendment No. 1 to a contract with **ALLIED ELECTRONICS, INC.**, Austin, TX for electrical repair parts to extend the contract for three 12-month periods in the amount to not to exceed \$45,000 with two additional 12-month extension options in an amount not to exceed \$45,000 per extension option, for a revised total contract amount not to exceed \$270,000. Sole bid received. Solicitation was extended to allow additional bidders time to respond, no other responses were received.

AMOUNT & SOURCE OF FUNDING: Funding in the amount of \$15,000 is available in the Fiscal Year 2010-2011 Operating Budget of the Aviation Department. Funding for the remaining four months of the original contract and extension options is contingent upon available funding in future budgets.

FISCAL NOTE: There is no unanticipated fiscal impact. A fiscal note is not required.

FOR MORE INFORMATION CONTACT: Brenda Helgren, Sr. Buyer/530-7533

PRIOR COUNCIL ACTION: N/A

BOARD AND COMMISSION ACTION: Reviewed by the Austin Airport Advisory Commission 04/12/11.

PURCHASING: Contract Amendment

<u>MBE/WBE</u>: This contract will be awarded in compliance with Chapter 2-9D of the City Code (Minority-Owned and Women-Owned Business Enterprise Procurement Program). No subcontracting opportunities were identified; therefore, no goals were established for this contract.

This agreement is for electrical and electronic repair/replacement parts for the various systems at the Airport to include baggage handling, security, boarding bridge, paging, and lighting and power monitoring.

This contract was competitively bid with a single response in 2008. This recommended Council action is to approve Amendment No. 1 for \$45,000 and the authorization to enter into the final two option periods for \$45,000 each when appropriate, for a final contract value of \$270,000.

Contract Summary		
Contract History	Description	Amount
Original Contract	36-month contract for electrical repair parts with 3-12 month extension options	\$45,000
Administrative action	Add funds for second year of contract	\$45,000
Administrative action	Add funds third year of contract	\$45,000
Proposed Amendment No. 1	Exercise the first extension	\$45,000

CITY OF AUSTIN
RECOMMENDATION FOR COUNCIL ACTIONPAGE 2 OF 2
VENDOR NAME: ALLIED ELECTRONICS, INC.

AGENDA DATE: 05/12/11

	option	
Remaining extension options	Two remaining 12-month extension option	\$90,000
	Total contract amount	\$270,000

CITY OF AUSTIN
RECOMMENDATION FOR COUNCIL ACTIONPAGE 1 OF 2
VENDOR NAME: KOCH FILTER CORPORATION

SUBJECT: Authorize award and execution of Amendment No. 2 to a contract with **KOCH FILTER CORPORATION**, Louisville, KY for air filters to extend the contract for one 12-month period in the amount to not to exceed \$24,402 with one additional 12-month extension options in an amount not to exceed \$24,402, for a total contract amount not to exceed \$144,216.

AMOUNT & SOURCE OF FUNDING: Funding in the amount of \$8,134 is available in the Fiscal Year 2010-2011 Operating Budget of the Aviation Department. Funding for the remaining four months of the first option and remaining extension options is contingent upon available funding in future budgets.

FISCAL NOTE: There is no unanticipated fiscal impact. A fiscal note is not required.

FOR MORE INFORMATION CONTACT: Brenda Helgren, Sr. Buyer/530-7533

PRIOR COUNCIL ACTION: N/A

BOARD AND COMMISSION ACTION: Reviewed by the Austin Airport Advisory Commission 04/12/11.

PURCHASING: Contract Amendment

<u>MBE/WBE</u>: This contract will be awarded in compliance with Chapter 2-9D of the City Code (Minority-Owned and Women-Owned Business Enterprise Procurement Program). No subcontracting opportunities were identified; therefore, no goals were established for this contract.

This agreement is for replacement HVAC air filters for all ABIA campus HVAC equipment. These filters are used as replacements to ensure removal of airborne contaminants while maintaining a good indoor air quality for our customers.

This contract was competitively bid and awarded in 2007. This recommended Council action is to approve Amendment No. 2 for \$24,402 and the authorization to enter into the final option period for \$24,402 each when appropriate, for a final contract value of \$144,216.

Contract Summary		
Contract History	Description	Amount
Original Contract	36-month contract for air filters with 3-12 month extension options	\$23,670
Administrative action	Add funds for second year of contract	\$23,670
Administrative action	Add funds third year of contract	\$23,670
Amendment No. 1	Exercise the first extension option	\$24,402

AGENDA DATE: 05/12/11

Proposed Amendment No. 2	Exercise the second extension option	\$24,402
Remaining extension option	One remaining 12-month extension option	\$24,402
	Total contract amount	\$144,216

CITY OF AUSTIN
RECOMMENDATION FOR COUNCIL ACTIONPAGE 1 OF 2
VENDOR NAME: FIVE STAR ELECTRIC MOTORS

<u>SUBJECT</u>: Authorize award and execution of Amendment No. 2 to a contract with **FIVE STAR ELECTRIC MOTORS**, San Antonio, TX for maintenance and repair parts for Robicon VFD's to extend the contract for one 12-month period in the amount to not to exceed \$13,400.00 with one additional 12-month extension option in an amount not to exceed \$13,400, for a total contract amount not to exceed \$80,400. Five Star Electric Motors is the sole source provider for after market parts of this equipment.

AMOUNT & SOURCE OF FUNDING: Funding in the amount of \$4,467 is available in the Fiscal Year 2010-2011 Operating Budget of the Aviation Department.

FISCAL NOTE: A fiscal note is not required.

FOR MORE INFORMATION CONTACT: Brenda Helgren, Sr. Buyer/530-7533

PRIOR COUNCIL ACTION: N/A

BOARD AND COMMISSION ACTION: Reviewed by the Austin Airport Advisory Commission 04/12/11.

PURCHASING: Contract Amendment.

<u>MBE/WBE</u>: This contract will be awarded in compliance with Chapter 2-9C of the City Code (Minority-Owned and Women-Owned Business Enterprise Procurement Program). No subcontracting opportunities were identified; therefore, no goals were established for this contract.

This agreement is for the maintenance and repair parts for the Robicon Variable Frequency Drives (VFD's) for the Airport's Central Plant. These VFD's are used to vary the motor speed for the buildings chilled water and heating hot water pumps which reduces the amount of electricity consumed to cool and heat the entire terminal facility.

This contract was issued as a sole source contract in 2007. Amendment No. 1 was issued in May, 2010 for the first extension option. This recommended Council action is to approve Amendment No. 2 for \$13,400 and the authorization to enter into the final option period for \$13,400 when appropriate, for a final contract value of \$80,400.

Contract Summary		
Contract History	Description	Amount
Original Contract	36-month contract for maintenance and repair parts for Robicon VFD's with 3-12 month extension options	\$13,400
Administrative action	Add funds for second year of contract	\$13,400
Administrative action	Add funds third year of contract	\$13,400
Amendment No. 1	Exercise the first extension option	\$13,400
Proposed Amendment No. 2	Exercise the second extension option	\$13,400
Remaining extension option	One remaining 12-month extension option	\$13,400
	Total contract amount	\$80,400

<u>SUBJECT</u>: Authorize award and execution of Amendment No. 1 to a contract **THE LENAPE GROUP dba VIGNEAUX CORPORTATION**, Jacksonville, FL for fire door barrel assemblies to extend the contract for one 12-month period in the amount to not to exceed \$20,000 with two additional 12-month extension option in an amount not to exceed \$20,000, for a total contract amount not to exceed \$100,000. The Lenape Group dba Vigneaux Corporation is the sole source provider for these parts.

<u>AMOUNT & SOURCE OF FUNDING</u>: Funding in the amount of \$6,667 is available in the Fiscal Year 2010-2011 Operating Budget of the Aviation Department. Funding for the remaining four months of the original contract and extension options is contingent upon available funding in future budgets.

FISCAL NOTE: A fiscal note is not required.

FOR MORE INFORMATION CONTACT: Brenda Helgren, Sr. Buyer/530-7533

PRIOR COUNCIL ACTION: N/A

BOARD AND COMMISSION ACTION: Reviewed by the Austin Airport Advisory Commission 04/12/11.

PURCHASING: Contract Amendment.

<u>MBE/WBE</u>: This contract will be awarded in compliance with Chapter 2-9D of the City Code (Minority-Owned and Women-Owned Business Enterprise Procurement Program). No subcontracting opportunities were identified; therefore, no goals were established for this contract.

This agreement is for the fire door barrel assemblies for the inbound and outbound baggage conveyor system. These replacement assemblies serve two purposes; act as a fire stop to prevent fire from spreading throughout the facility and to provide a security barrier between the secure and non-secure areas of ABIA.

This contract was issued as a sole source contract in 2009. This recommended Council action is to approve an administrative increase in an amount not to exceed \$20,000 for the final 12-months of the initial 36-month contract and the authorization to enter into the final option periods for \$20,000 each when appropriate, for a final contract value of \$100,000.

CITY OF AUSTIN RECOMMENDATION FOR COUNCIL ACTIONPAGE 2 OF 2 VENDOR NAME: THE LENAPE GROUP dba VIGNEAUX CORPORATION

Contract Summary		
Contract History	Description	Amount
Original Contract	36-month contract for ground power cables and end connectors (\$60,000 for initial 36-Month period, or \$20,000 Annually)	\$20,000
Administrative action	Add funds for second year of contract	\$20,000
	Cumulative Amount to Date:	\$40,000
Proposed Administrative Increase	Allow administrative increase to contract for the remaining 12-months of the initial 36-month contract.	\$20,000
Remaining extension options	Two remaining 12-month extension options	\$40,000
	Total contract amount	\$100,000
