JOURNEY WITH AUS

Journey With AUS
Latest Updates



Airport Advisory Commission
January 2026

Lyn Estabrook
Deputy Chief – Planning & Development

Table of Contents

Project Updates

- West Infill
- West Gate Expansion
- Yellow Garage
- Atrium Infill
- New Midfield Taxiways



JOURNEY WITH AUS

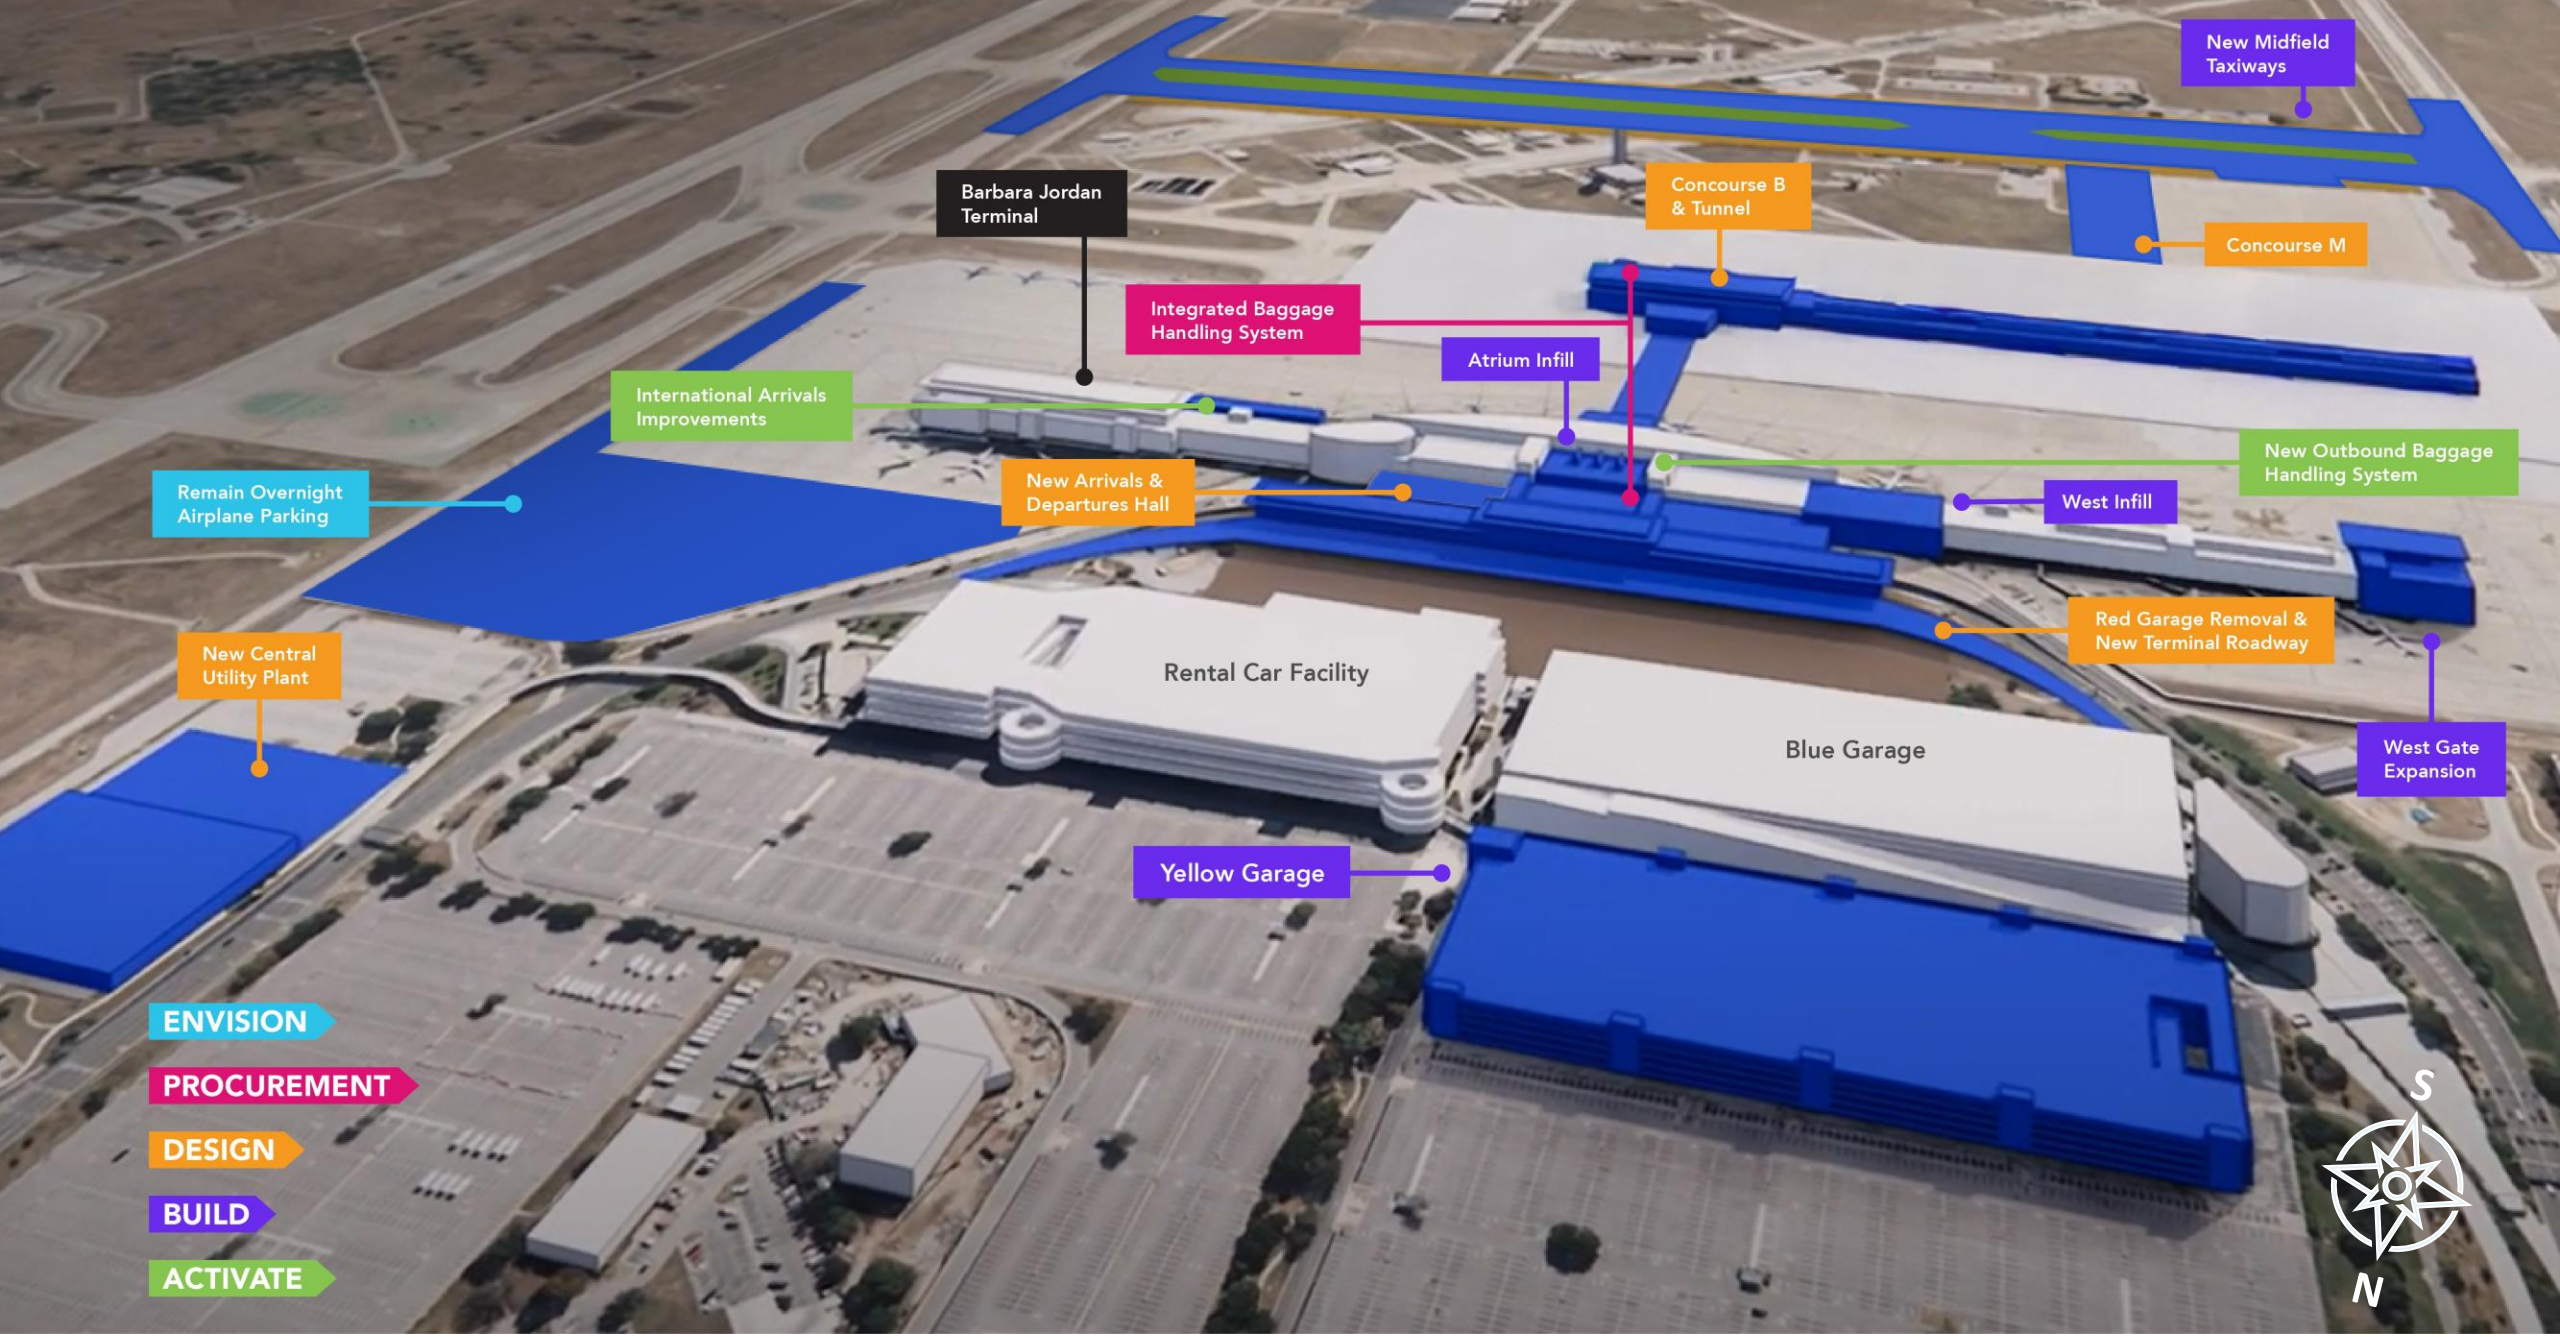
New Midfield Taxiways
Barbara Jordan Terminal
Concourse B & Tunnel
Concourse M
Integrated Baggage Handling System
Atrium Infill
International Arrivals Improvements
New Outbound Baggage Handling System
Remain Overnight Airplane Parking
New Arrivals & Departures Hall
West Infill
Red Garage Removal & New Terminal Roadway
New Central Utility Plant
Rental Car Facility
Blue Garage
West Gate Expansion
Yellow Garage
ENVISION
PROCUREMENT
DESIGN
BUILD
ACTIVATE
S
N

West Infill

Design-Build:
Gensler/Whiting Turner

BUILD

Latest Updates

- Outbound Baggage Handling System is complete and performing well
- Contractor is completing finishing touches
- Mechanical, electrical and building systems quality assurance continues

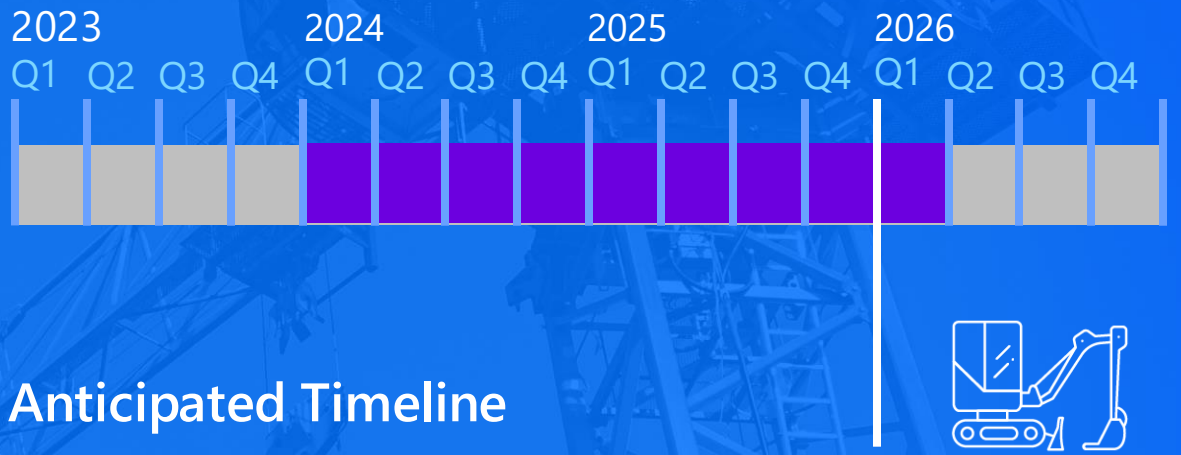

Anticipated Timeline

Build: Q1 2024 – Q1 2026

NEXT PHASE: ACTIVATE

Enabling Project: New Arrivals & Departures Hall

Monumental Stairs Work Continues

West Gate Expansion

Designer: Page
Contractor: Hensel Phelps

BUILD

Latest Updates

- Interior finishes continue with terrazzo flooring and interior metal panels nearing completion
- Testing of the building systems is ongoing
- Furniture has been delivered and is ready to install
- Bathroom tile and fixtures are nearing completion

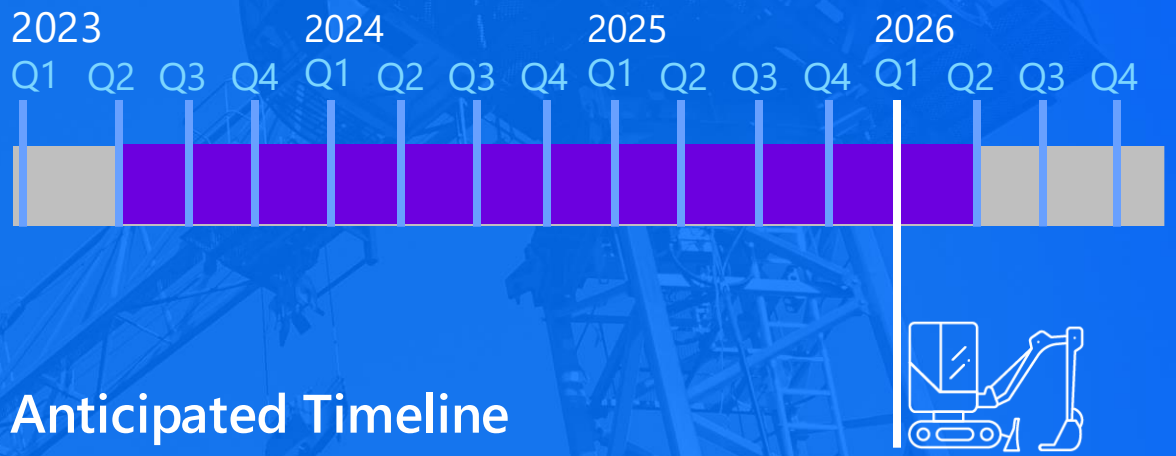

Anticipated Timeline

Build: Q2 2023 – Q1 2026

NEXT PHASE: ACTIVATE

Enabling Project: Concourse B & Tunnel

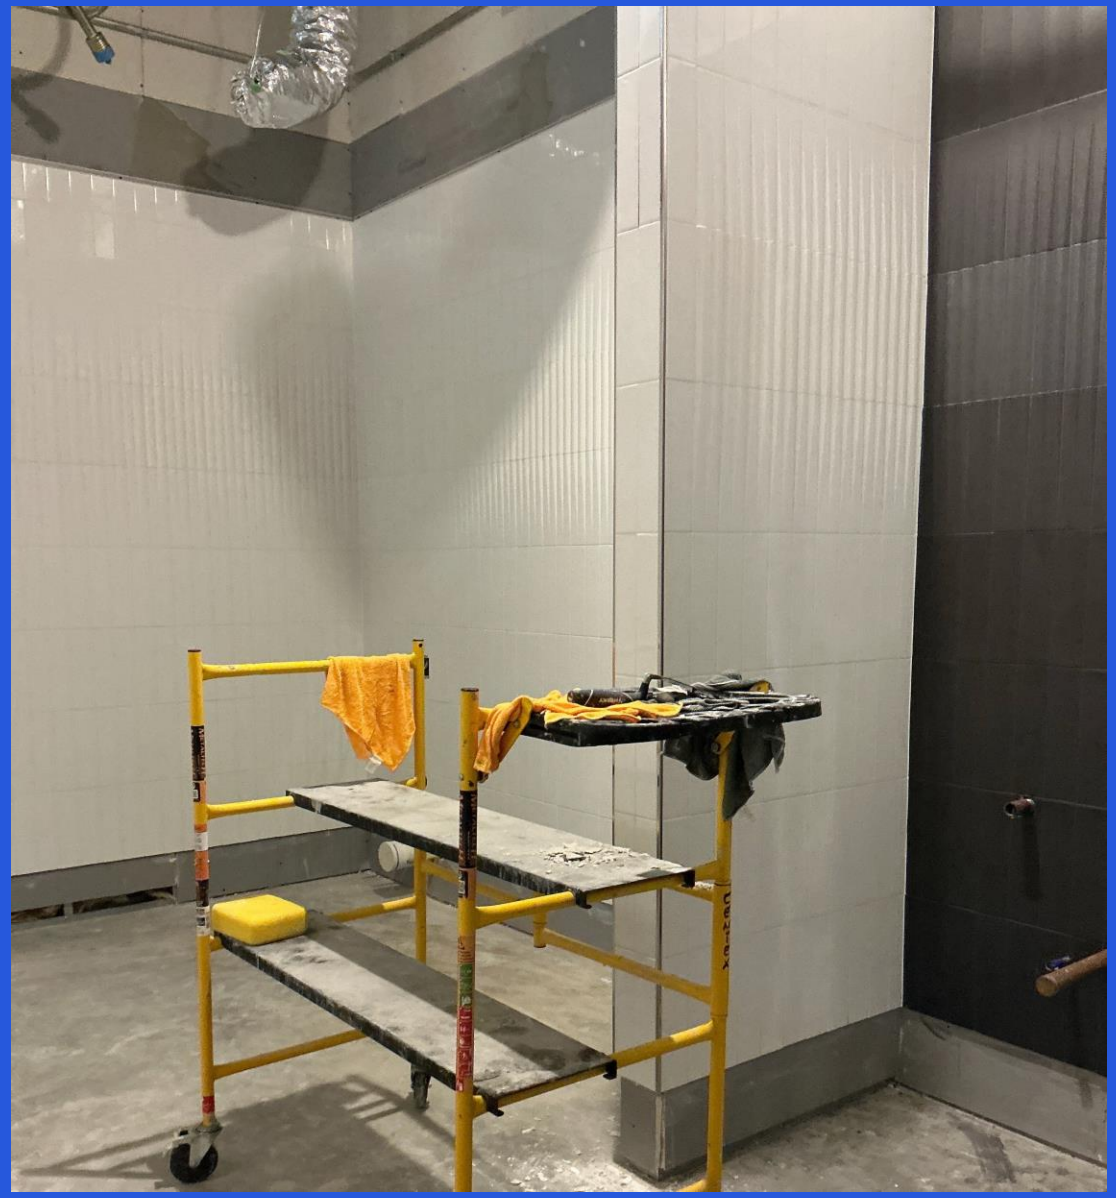

West Gate Expansion Mezzanine Level Restroom and Metal Panels Progress

Parking and Landside: Yellow Garage

Designer: PGAL
Contractor: Austin Commercial

BUILD

Latest Updates

- Completed drilling 447 of 456 piers
- Completed 40% of deck pours
- 50% of precast concrete spandrels installed on southside of the garage
- 20% of permanent concrete stairs installed
- Started roadway and north half vertical construction

Anticipated Timeline

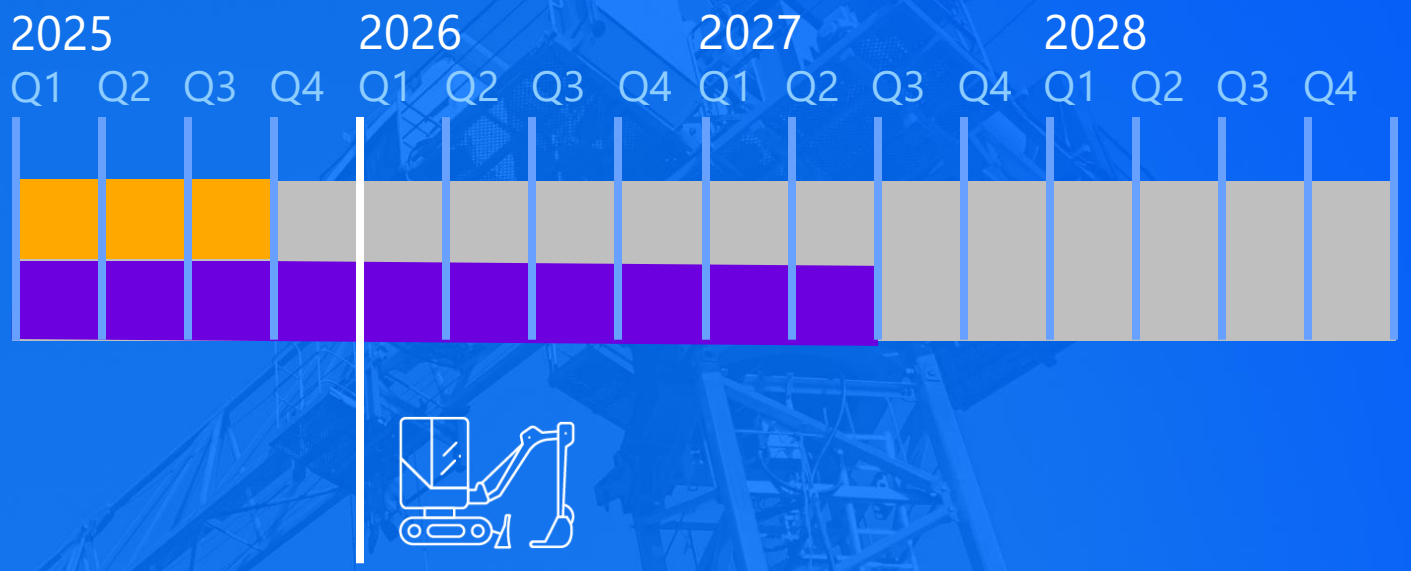

Design: Q3 2024 – Q3 2025

Build: Q1 2025 – Q3 2027

NEXT PHASE: ACTIVATE

Enabling Projects: Red Garage Removal & New Terminal Roadway, New Arrivals & Departures Hall

Yellow Garage southside including ramp construction and precast panels

Yellow Garage westside

Yellow Garage northside including north half vertical construction

Atrium Infill

Designer: Corgan
Contractor: Whiting-Turner

BUILD

Latest Updates

- Concrete pours are complete
- Demolition of south wall handrailing is ongoing
- Hanging scaffold will begin to be installed after the concrete is strong enough to hold
- Coordination with Art In Public Places and Clear Channel continues

Anticipated Timeline

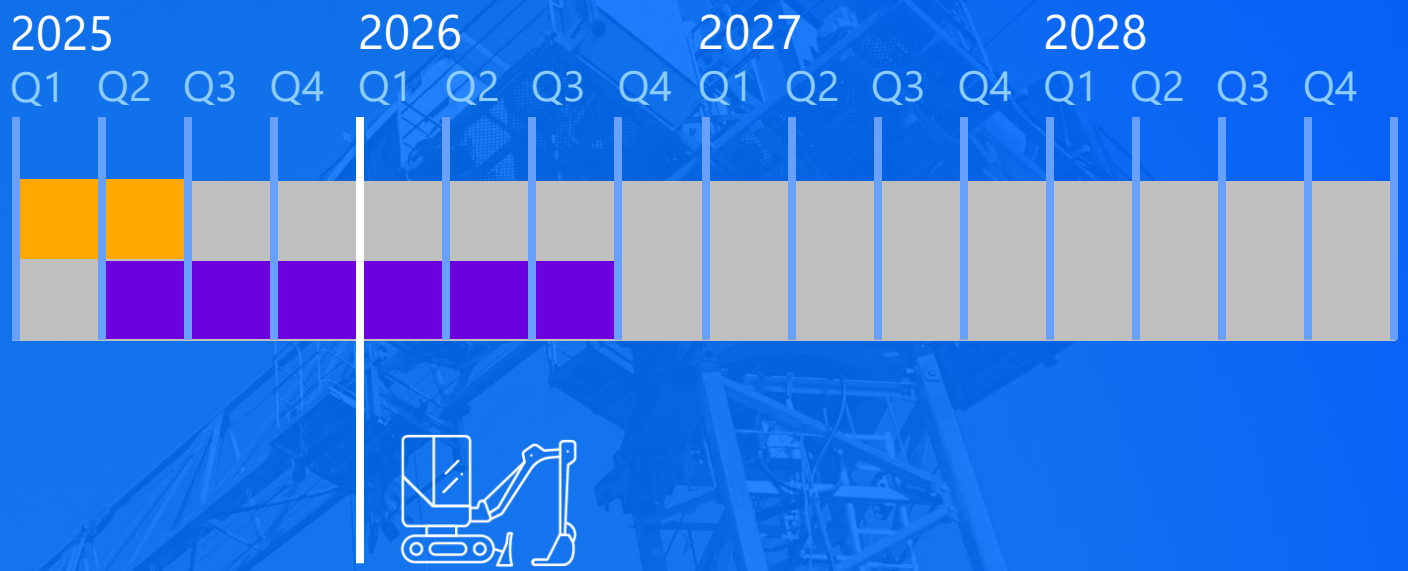

Design: Q2 2024 – Q2 2025

Build: Q2 2025 – Q3 2026

NEXT PHASE: ACTIVATE

Enabling Project: New Arrivals & Departures Hall

Concrete Placement Complete

New Midfield Taxiways & Maintenance Ramp Expansion

RS&H

Designer: RS&H
Contractor: Austin Bridge and Road

BUILD

Latest Updates

- Continued Phase 1 installation of Water Line A
- Continued Phase 3 drainage installation
- Continued Phase 4 Taxiway B closure for panel removals
- Finishing Taxiway P Bridge drill shafts

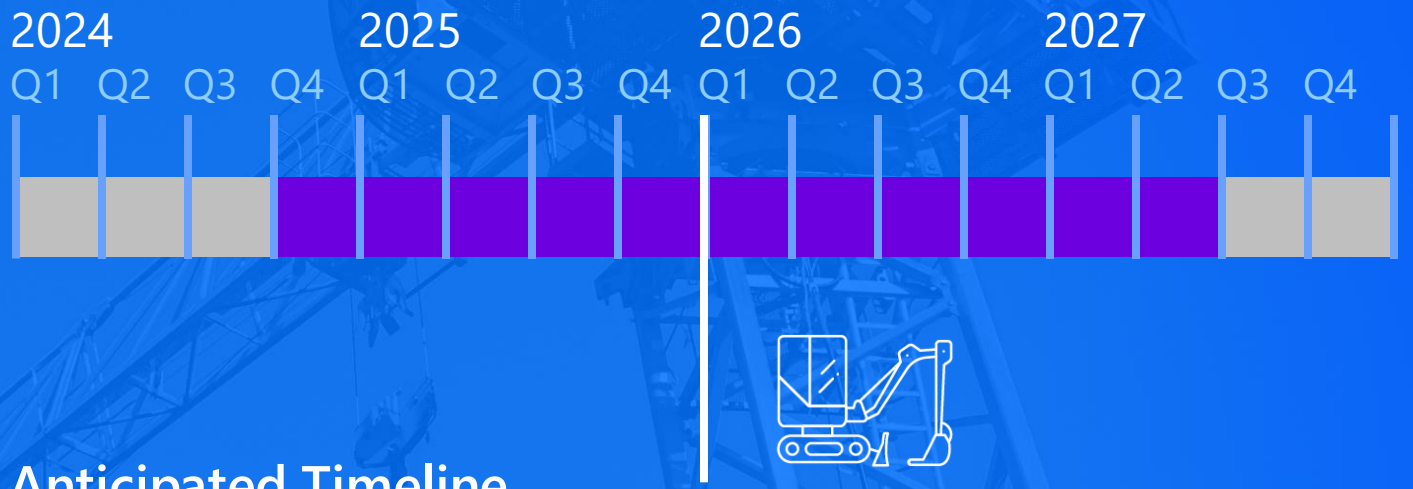

Anticipated Timeline

Build: Q4 2024 – Q2 2027

NEXT PHASE: ACTIVATE

Enabling Projects: Concourse B & Tunnel

Taxiway panel removal

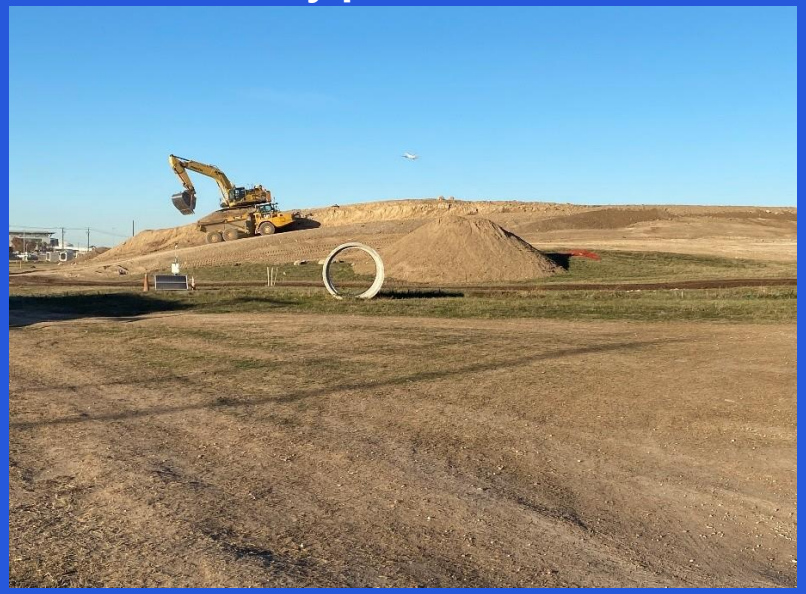

Embankment operations

Water utility installation

Prime Designers and Contractors

Project	Contract Type	Company
West Infill	Design-Build	Gensler/Whiting-Turner
West Gate Expansion	Design	Page
	CMAR	Hensel Phelps
Atrium Infill	Design	Corgan
	CMAR	Whiting Turner
New Midfield Taxiways	Design	RS&H
	CMAR	Austin Bridge & Road
Yellow Garage	Design	PGAL
	CMAR	Austin Commercial
New Central Utility Plant	Design-Build	JE Dunn/Jacobs
Utility Infrastructure Campus-Wide	Design	HDR
	CMAR	Sundt/Archer Western
Concourse B & Tunnel	Design	Page/Fentress
	CMAR	Hensel-Phelps
New Arrivals & Departures Hall	Design	SOM
	CMAR	Austin Commercial

Thank You!

JOURNEY WITH AUS
